

GREAT WATER ALLIANCE

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines



Waukesha Water Utility


Owner

Super Excavators, Inc.


General Contractor

\$33,934,739

Original Contract Amount



Pipeline Installed (LF)




Invoiced to Date


Milestone	Contract Date
Notice to Proceed	October 19, 2020
Substantial Completion	August 15, 2023
Final Completion	October 14, 2023

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	125
Days Until DOJ 50% Compliance Certification	276
Days Until DOJ Program Final Completion	626


Data current through Friday, April 9, 2021




Notice of Noncompliance

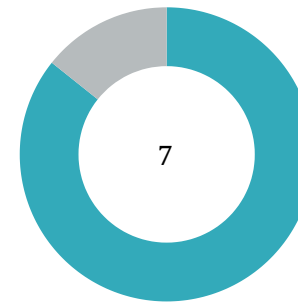


Stakeholder Engagement

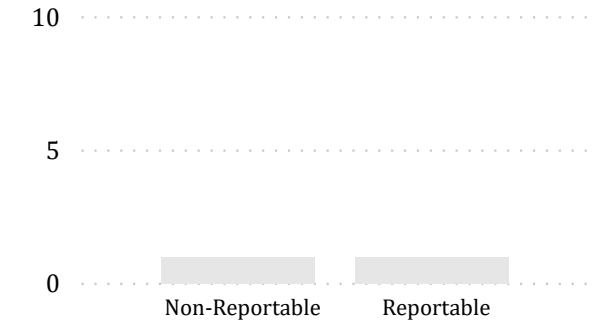

Safety

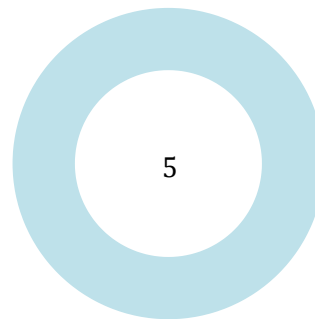


Change Orders

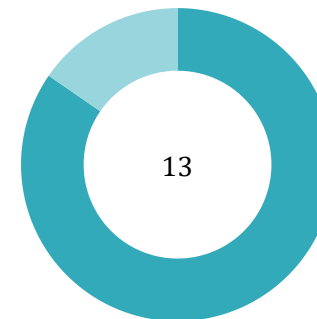

RFIs

8
Average of Turnaround

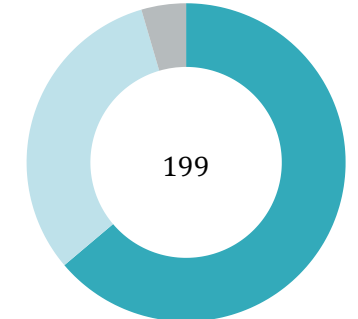

Engineering Submittals

12
Average of Turnaround
1
Excessive Reviews

● None at this time
 ● Open, Submitted
 ● Pending
 ● Closed, Approved
 ● Rejected, Withdrawn


PIPELINE PROGRESS

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines



Data current through:

Weekly Report Ending
Friday, April 9, 2021

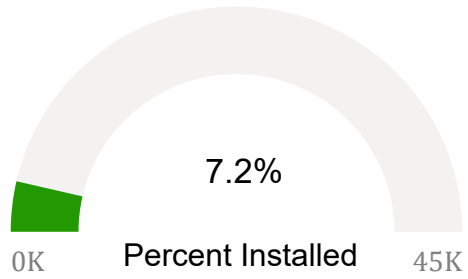


3247
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, April 9, 2021

5000
Forecast Pipe Progress (LF)

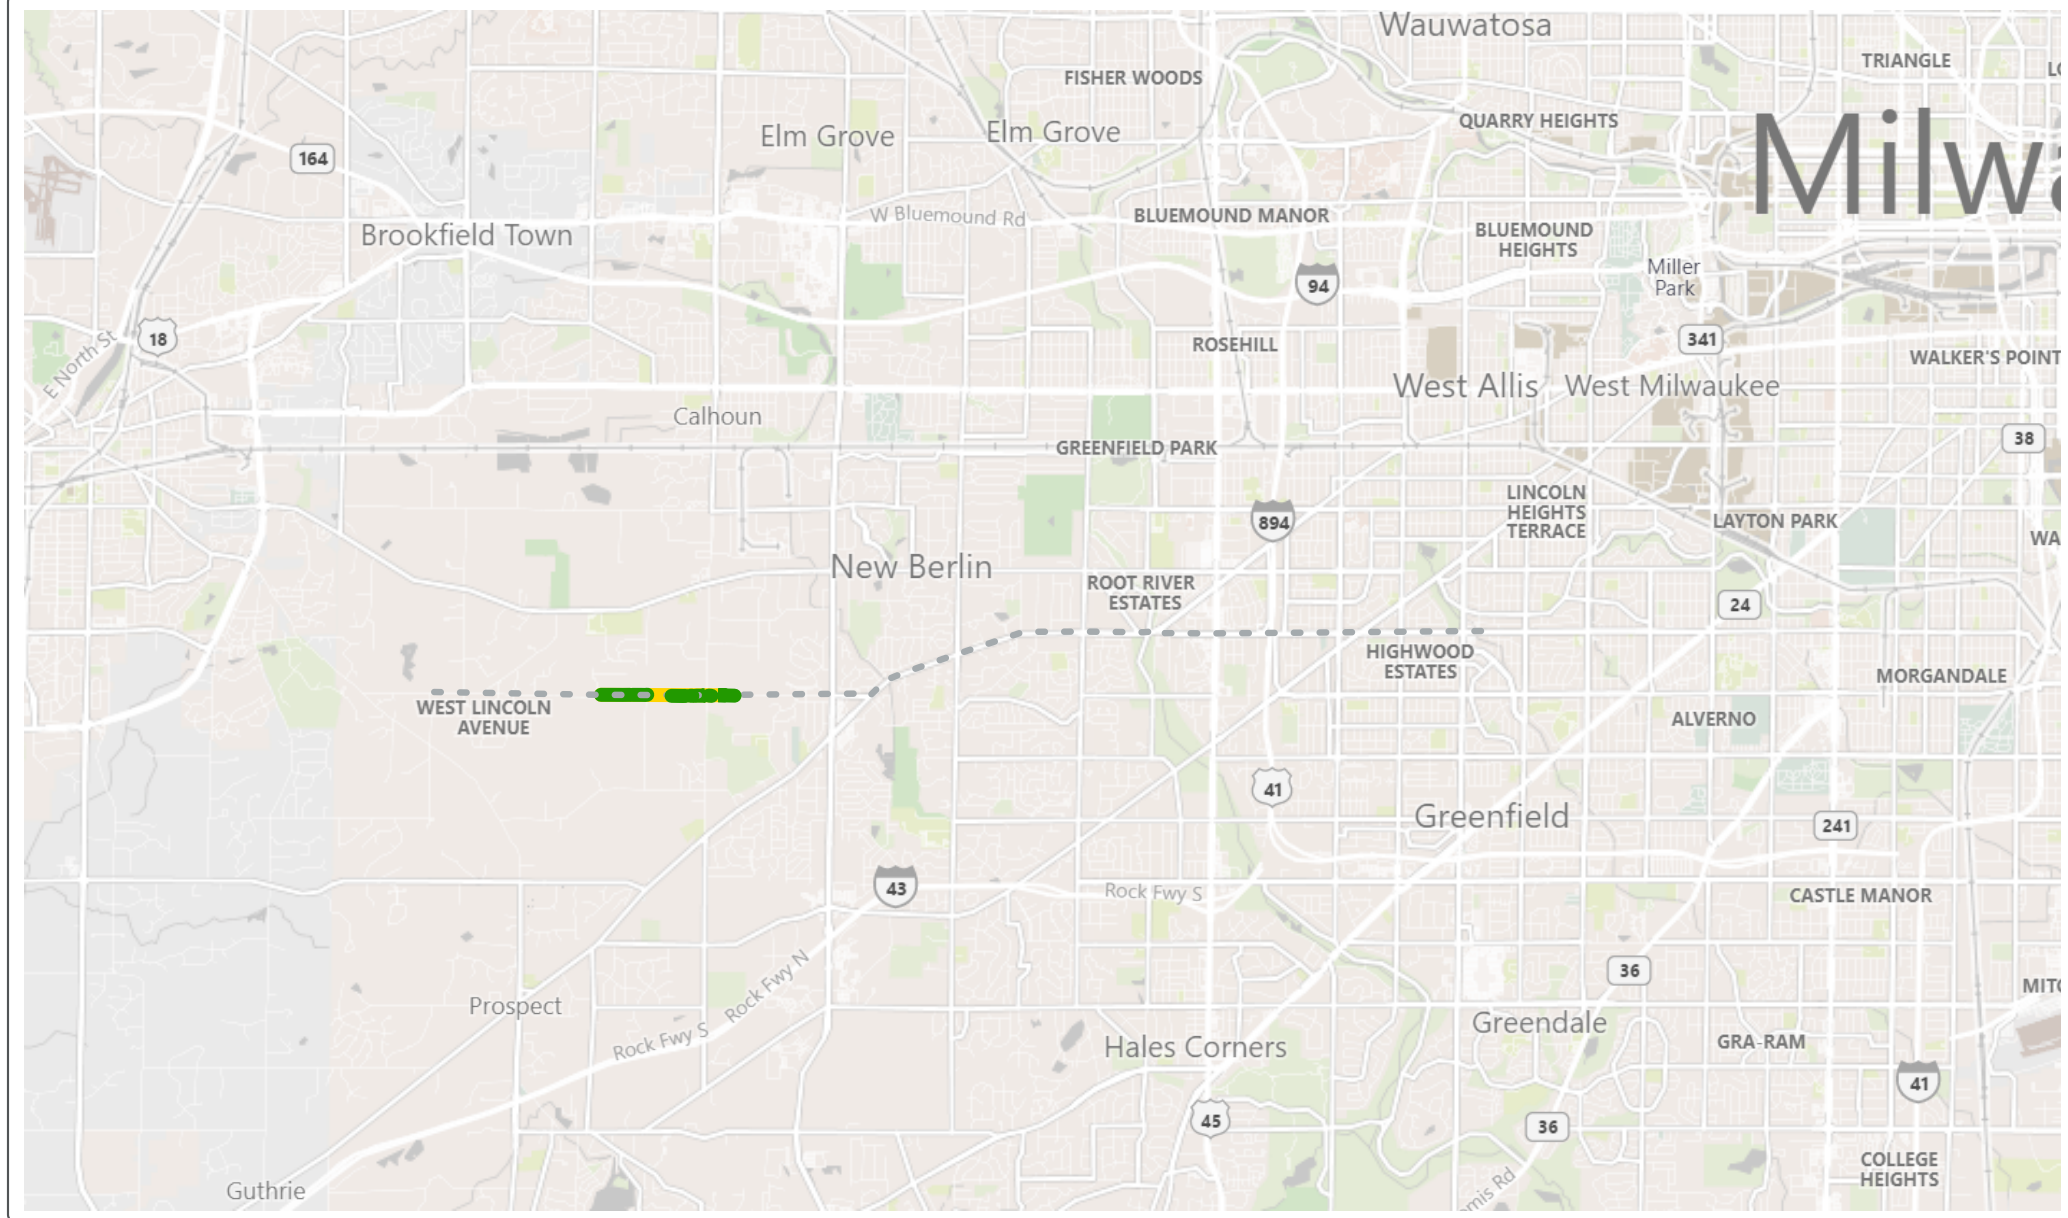

● Pipeline Route ● Installed Pipeline ● Forecast Construction

GREAT WATER ALLIANCE



CP5 - Return Flow Pipeline

Waukesha Water Utility


Owner

S. J. Louis Construction, Inc.


General Contractor

\$33,698,000

Original Contract Amount



Pipeline Installed (LF)




Invoiced to Date


Milestone	Contract Date
Notice to Proceed	July 1, 2020
Substantial Completion	March 23, 2022
Final Completion	May 22, 2022

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	203
Days Until DOJ 50% Compliance Certification	276
Days Until DOJ Program Final Completion	626


Data current through Friday, April 9, 2021

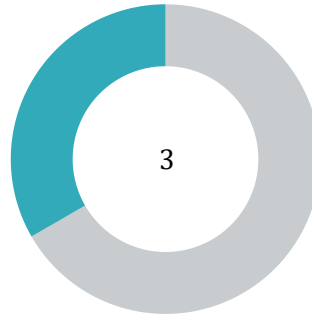


Notice of Noncompliance

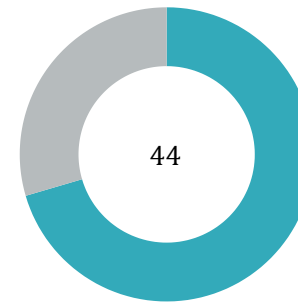


Stakeholder Engagement

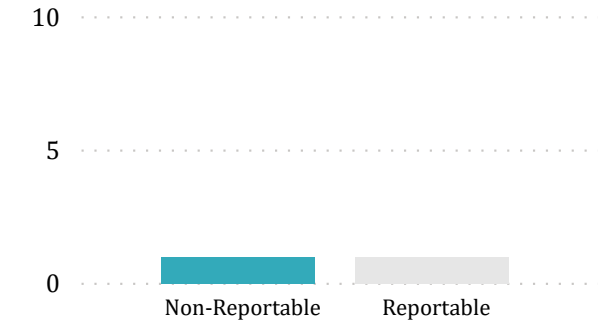

Safety




Change Orders

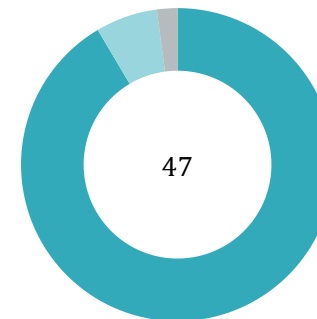

RFIs

4
Average of Turnaround

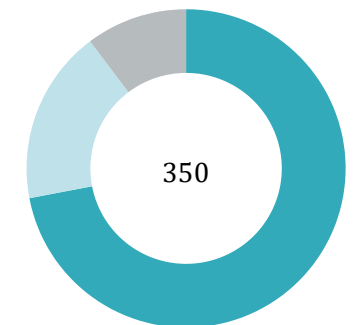

Engineering Submittals

13
Average of Turnaround
5
Excessive Reviews

● None at this time
 ● Open, Submitted
 ● Pending
 ● Closed, Approved
 ● Rejected, Withdrawn


PIPELINE PROGRESS

CP5 - Return Flow Pipeline



Data current through:

Weekly Report Ending
Friday, April 9, 2021

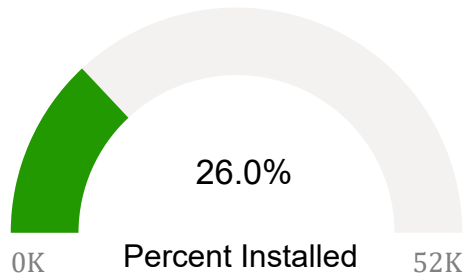


14K
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, April 9, 2021

36K
Forecast Pipe Progress (LF)

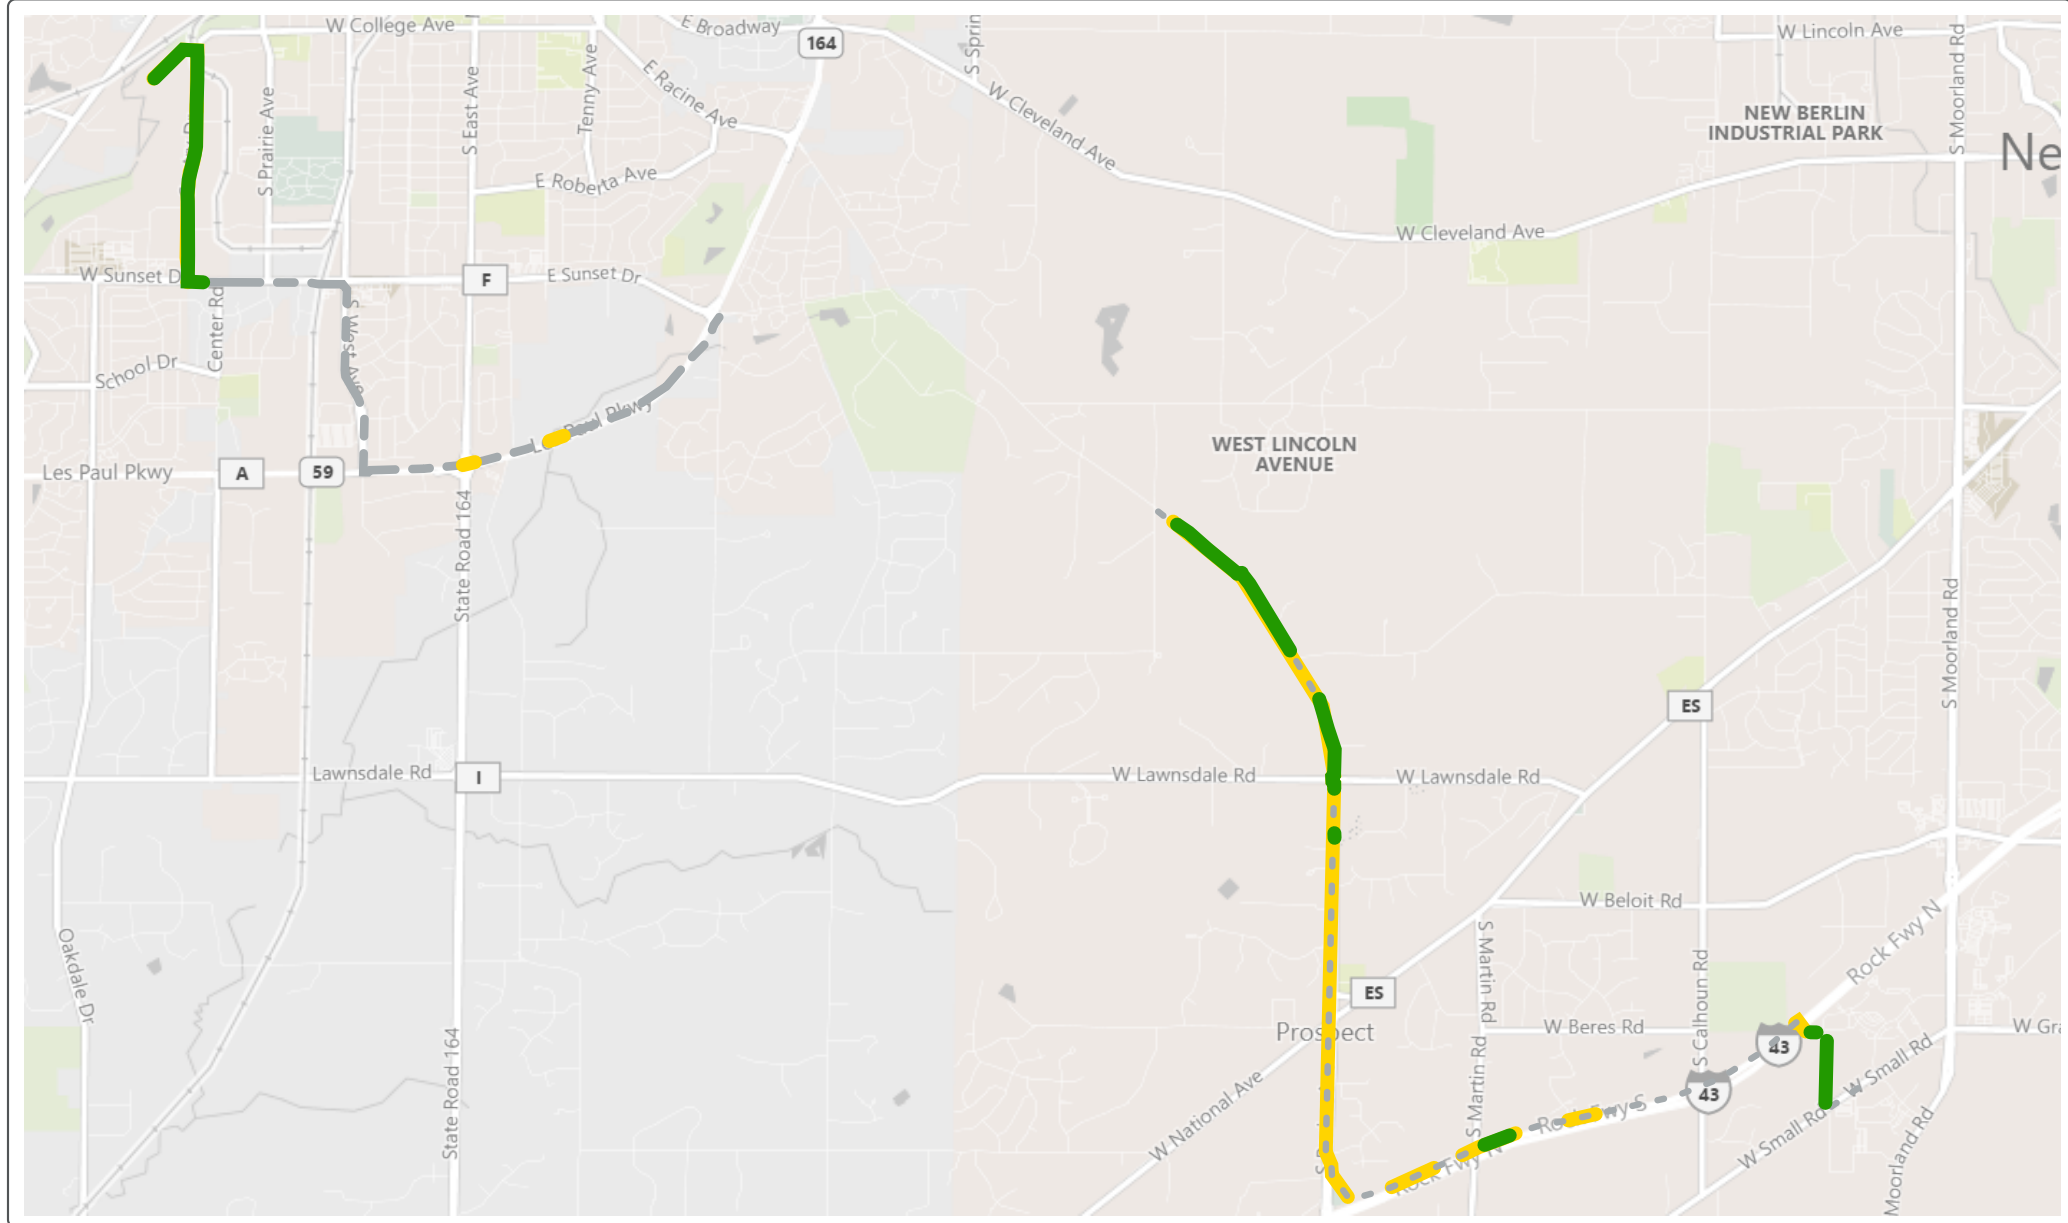

● Pipeline Route ● Installed Pipeline ● Forecast Construction

GREAT WATER ALLIANCE



CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities

Waukesha Water Utility


Owner

S. J. Louis Construction, Inc.


General Contractor

\$59,209,250

Original Contract Amount



Pipeline Installed (LF)




Invoiced to Date


Milestone	Contract Date
Notice to Proceed	July 1, 2020
Substantial Completion	April 22, 2022
Final Completion	June 21, 2022

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	203
Days Until DOJ 50% Compliance Certification	276
Days Until DOJ Program Final Completion	626


Data current through Friday, April 9, 2021

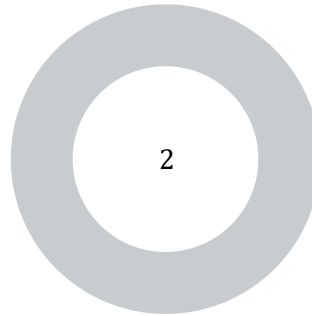


Notice of Noncompliance

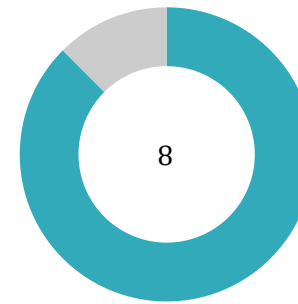


Stakeholder Engagement

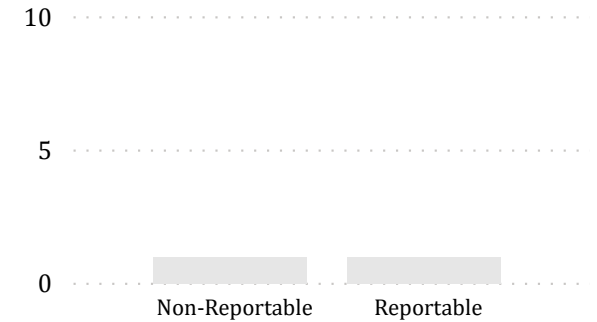

Safety




Change Orders

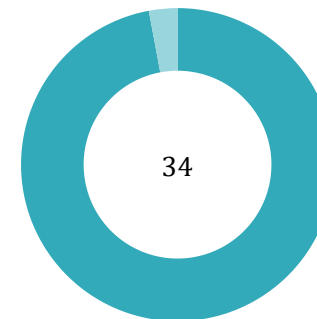

RFIs

5
Average of Turnaround

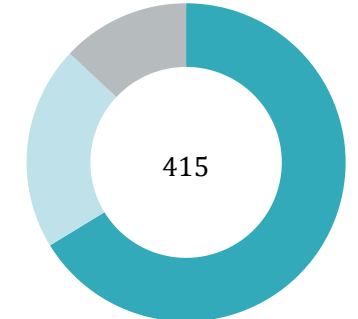

Engineering Submittals

14
Average of Turnaround
3
Excessive Reviews

● None at this time
 ● Open, Submitted
 ● Pending
 ● Closed, Approved
 ● Rejected, Withdrawn


PIPELINE PROGRESS

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities



Data current through:

Weekly Report Ending
Friday, April 9, 2021

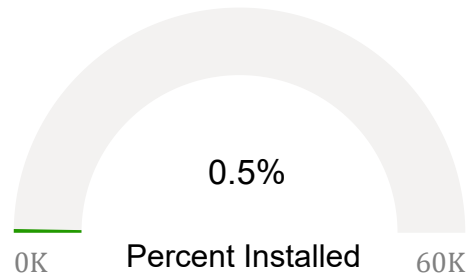

316
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, April 9, 2021

1952
Forecast Pipe Progress (LF)

