



GREAT WATER ALLIANCE

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines

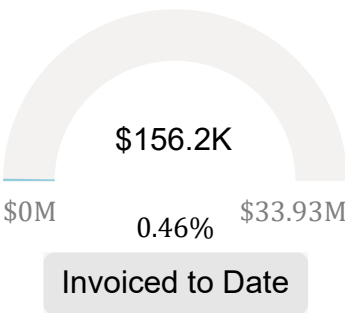


Waukesha Water Utility
Owner
Super Excavators, Inc.
General Contractor
\$33,934,739
Original Contract Amount

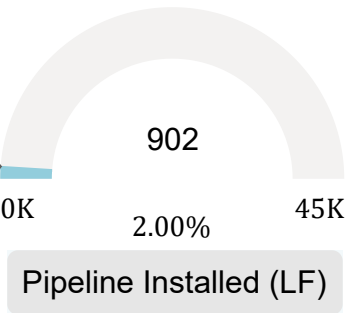


| Milestone | Contract Date |
|------------------------|------------------|
| Notice to Proceed | October 19, 2020 |
| Substantial Completion | August 15, 2023 |
| Final Completion | October 14, 2023 |

| Milestone Progression | Work Days |
|---|-----------|
| Days Added by Change Order | 0 |
| Days Since Notice to Proceed | 87 |
| Days Until DOJ 50% Compliance Certification | 314 |
| Days Until DOJ Program Final Completion | 664 |



Data current through Monday, February 15, 2021

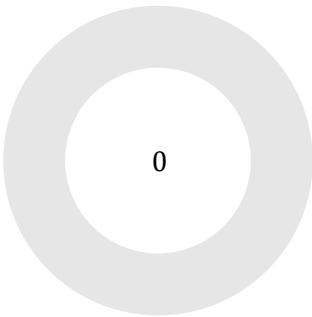


Notice of Violation

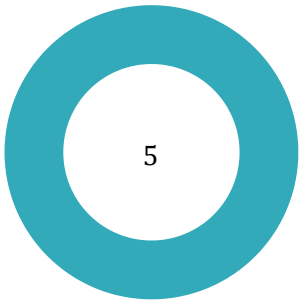

Stakeholder Engagement

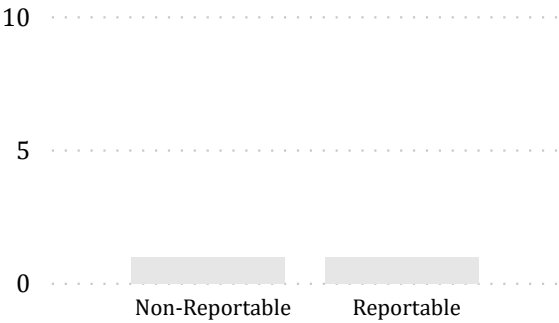


Change Orders

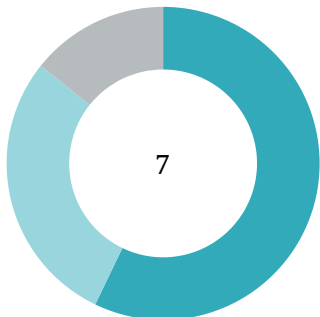

RFIs

2
Average of Turnaround

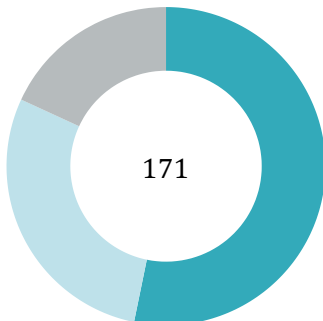

Engineering Submittals

0
Total Excessive Review

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines




Data current through:

Weekly Report Ending
Friday, February 12, 2021

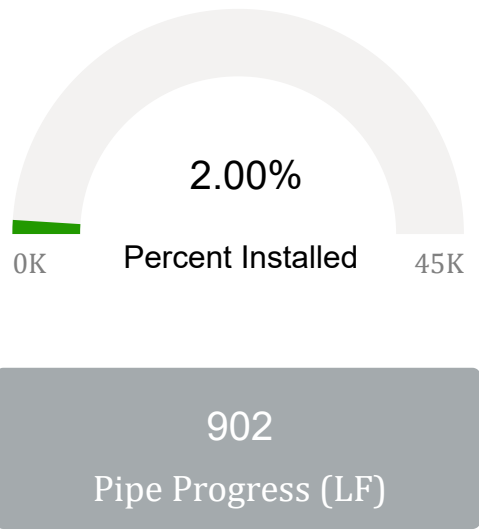

Data current through:

5-Week Look Ahead
Wednesday, February 10, 2021

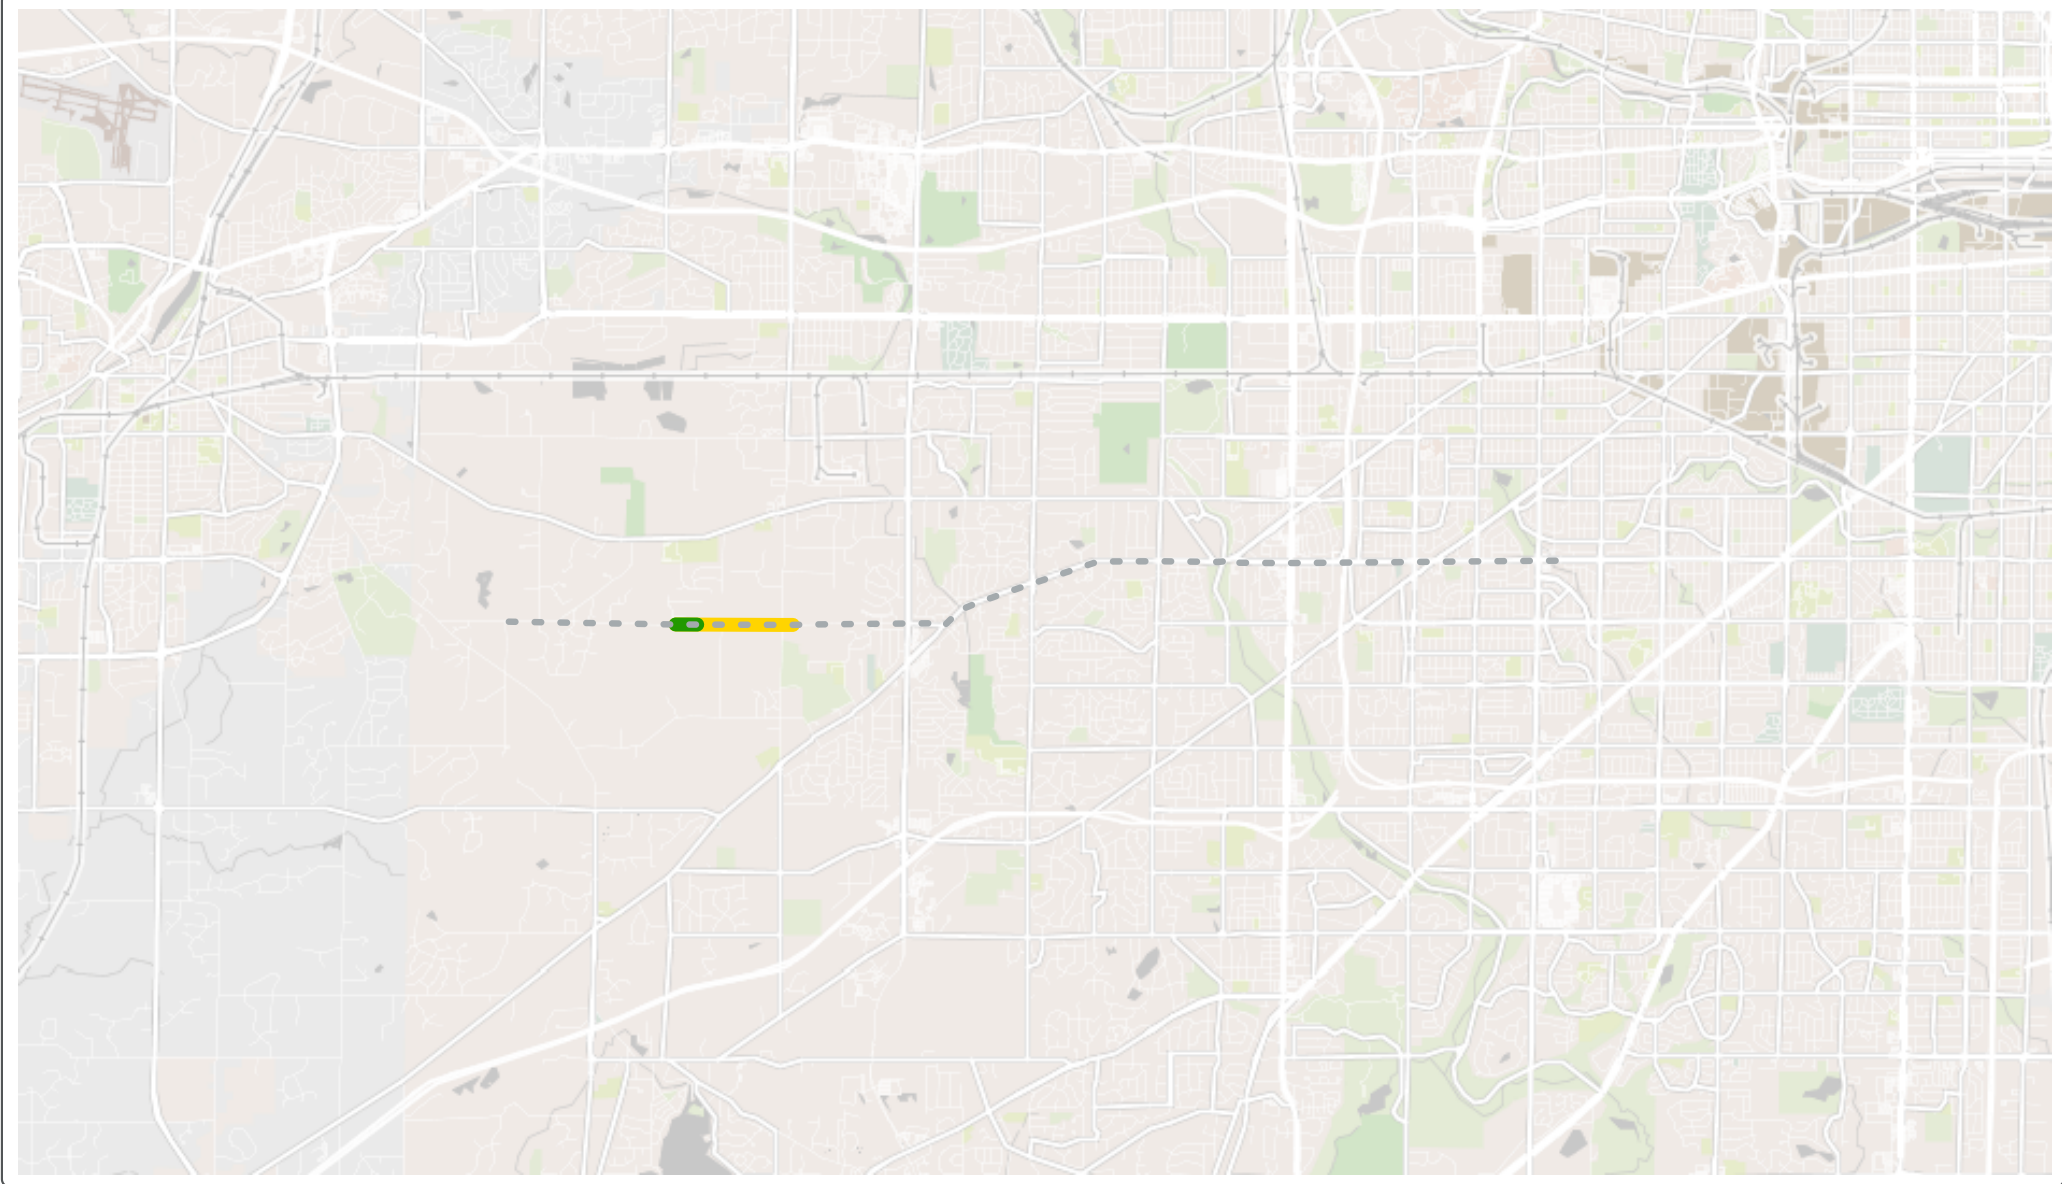

- Pipeline Route
- Installed Pipeline
- Forecast Construction

GREAT WATER ALLIANCE

CP5 - Return Flow Pipeline



Waukesha Water Utility


Owner

S. J. Louis Construction, Inc.

General Contractor


\$33,698,000

Original Contract Amount



0K 8.79% 52K

Pipeline Installed (LF)




\$0M 4.63% \$33.7M

Invoiced to Date


| Milestone | Contract Date |
|------------------------|----------------|
| Notice to Proceed | July 1, 2020 |
| Substantial Completion | March 23, 2022 |
| Final Completion | May 22, 2022 |

| Milestone Progression | Work Days |
|---|-----------|
| Days Added by Change Order | 0 |
| Days Since Notice to Proceed | 165 |
| Days Until DOJ 50% Compliance Certification | 314 |
| Days Until DOJ Program Final Completion | 664 |


Data current through Monday, February 15, 2021




Notice of Violation

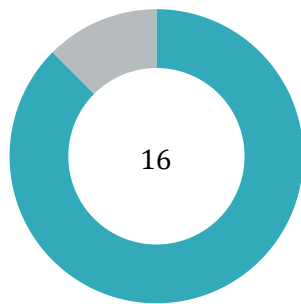


Stakeholder Engagement

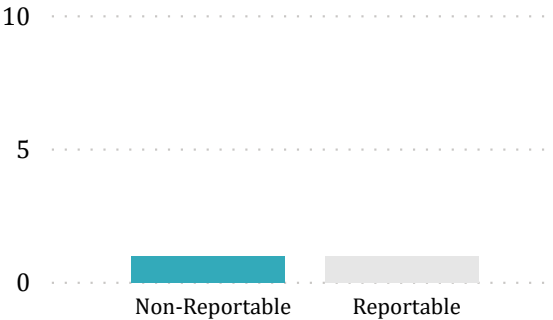

Safety




Change Orders

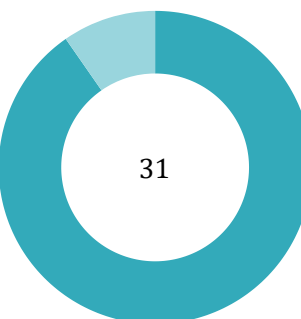

RFIs

3
Average of Turnaround

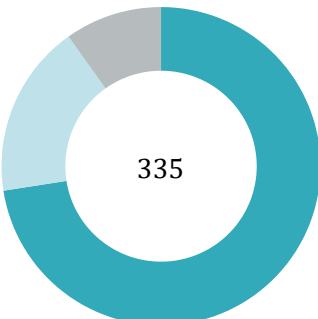

Engineering Submittals

0
Total Excessive Review

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP5 - Return Flow Pipeline



Data current through:

Weekly Report Ending
Friday, February 12, 2021

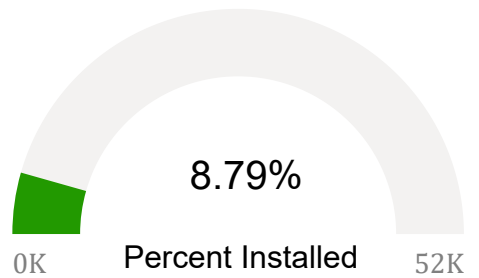


4590
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Wednesday, February 10, 2021

36K
Forecast Pipe Progress (LF)

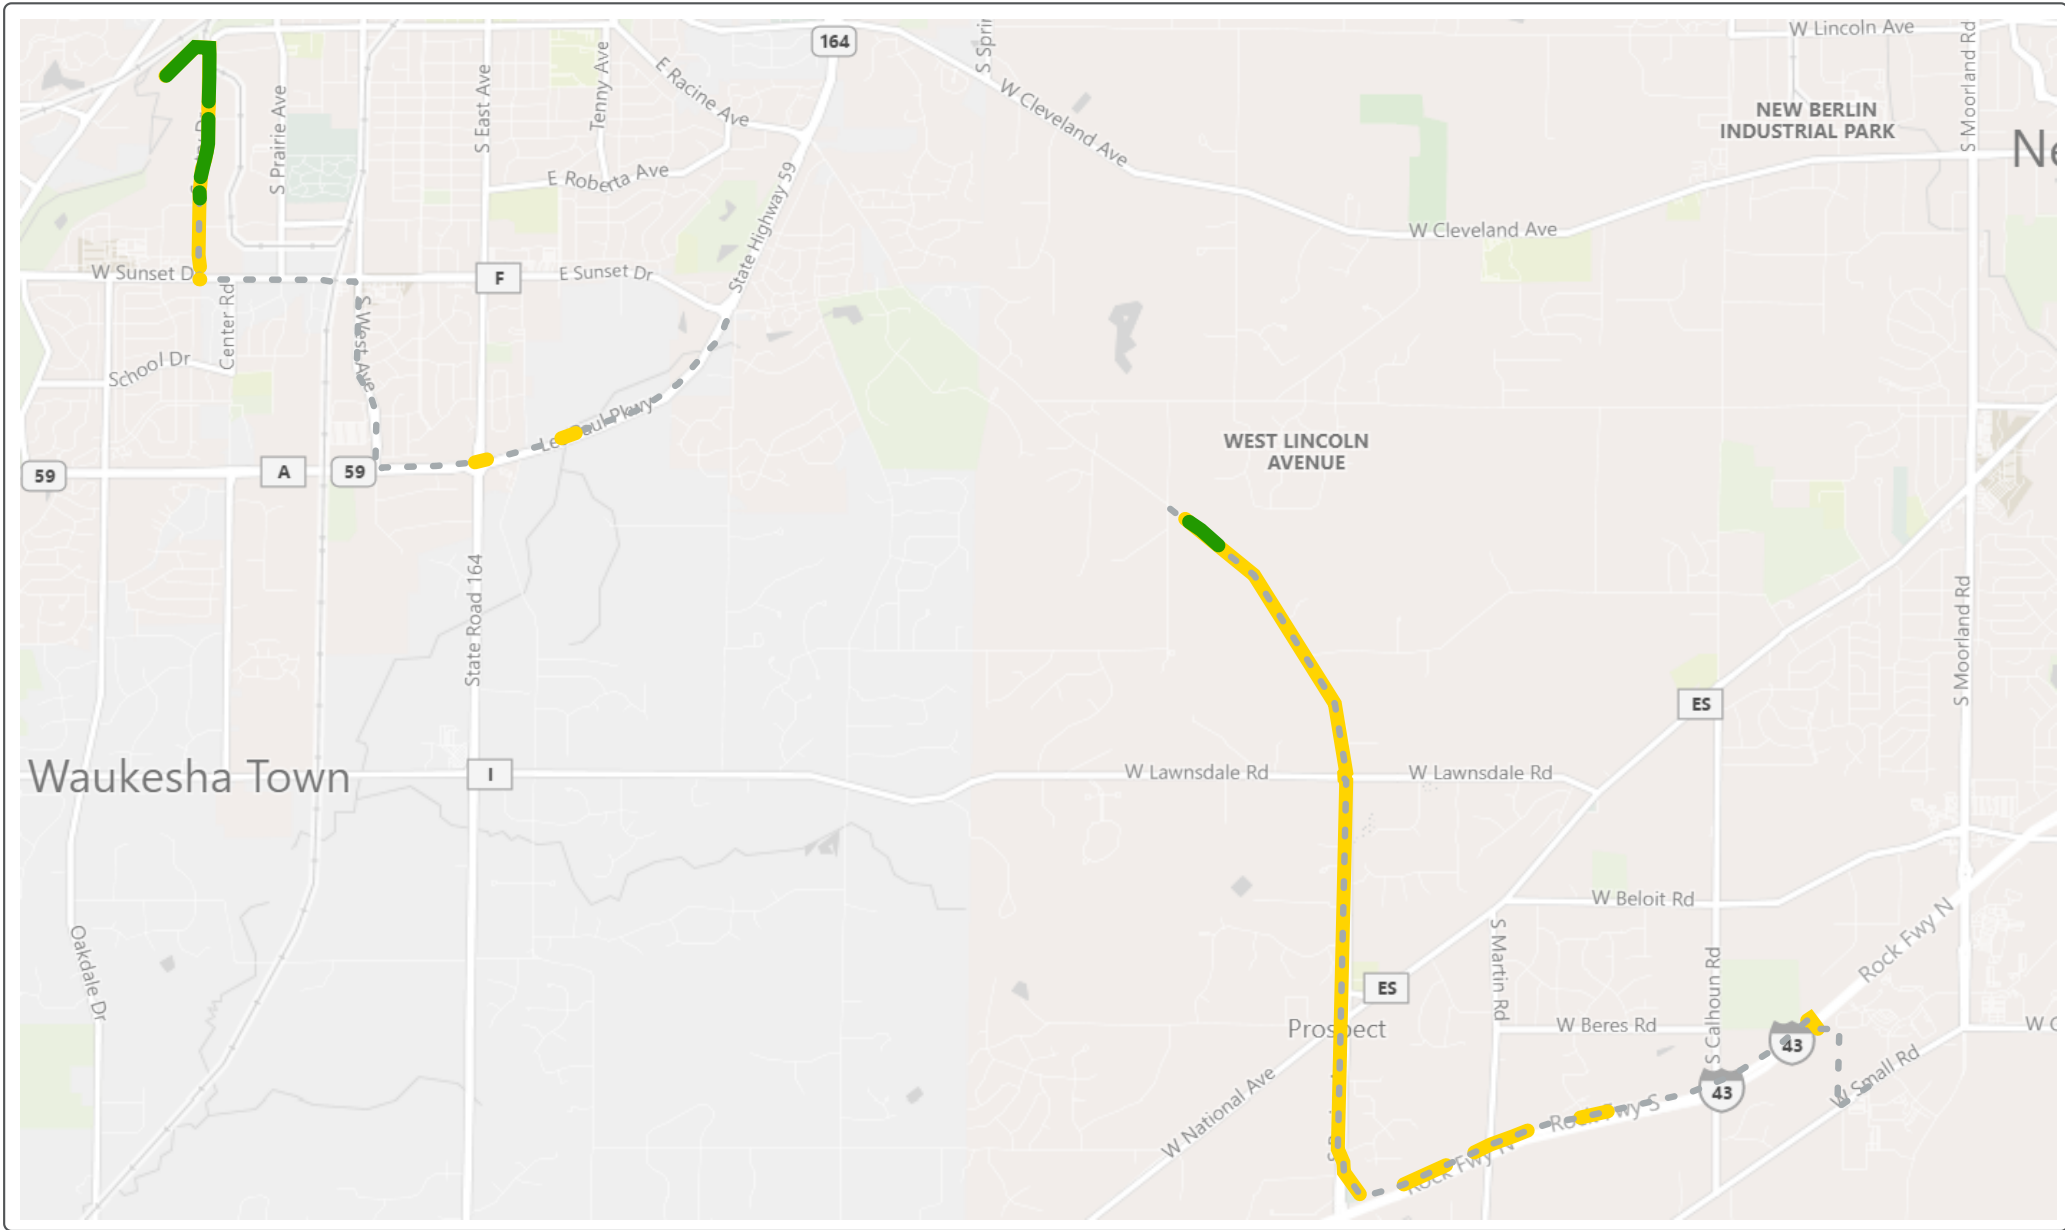



● Pipeline Route ● Installed Pipeline ● Forecast Construction

GREAT WATER ALLIANCE

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities




Waukesha Water Utility
Owner
S. J. Louis Construction, Inc.
General Contractor
\$59,209,250
Original Contract Amount

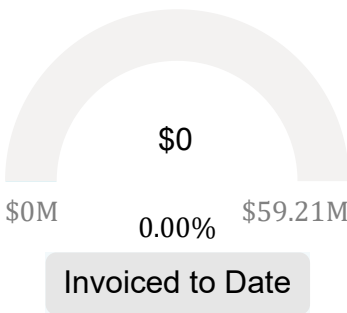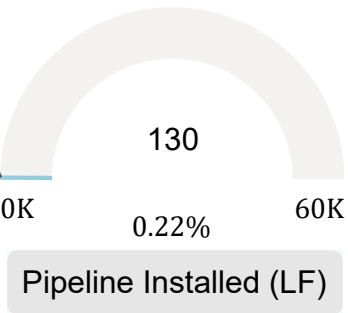


| Milestone | Contract Date |
|------------------------|----------------|
| Notice to Proceed | July 1, 2020 |
| Substantial Completion | April 22, 2022 |
| Final Completion | June 21, 2022 |

| Milestone Progression | Work Days |
|---|-----------|
| Days Added by Change Order | 0 |
| Days Since Notice to Proceed | 165 |
| Days Until DOJ 50% Compliance Certification | 314 |
| Days Until DOJ Program Final Completion | 664 |



Data current through Monday, February 15, 2021

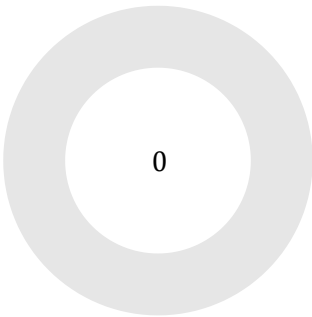


Notice of Violation

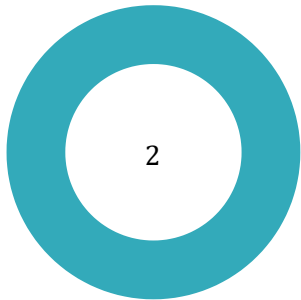

Stakeholder Engagement

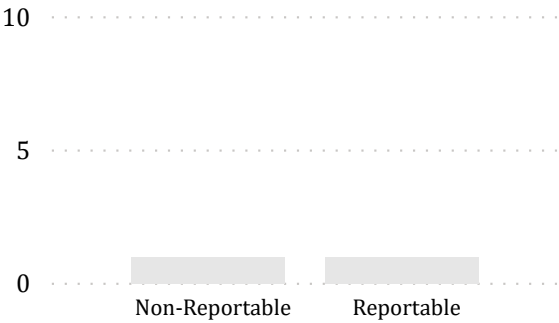


Change Orders

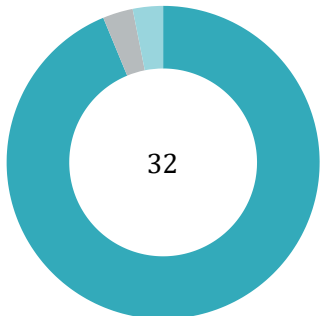

RFIs

5
Average of Turnaround

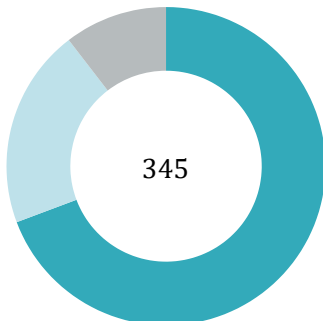

Engineering Submittals

0
Total Excessive Review

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities



Data current through:

Weekly Report Ending
Friday, February 12, 2021

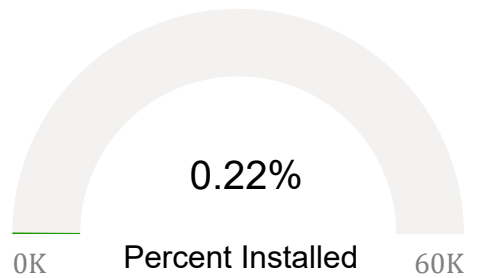


130
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Wednesday, February 10, 2021

1952
Forecast Pipe Progress (LF)

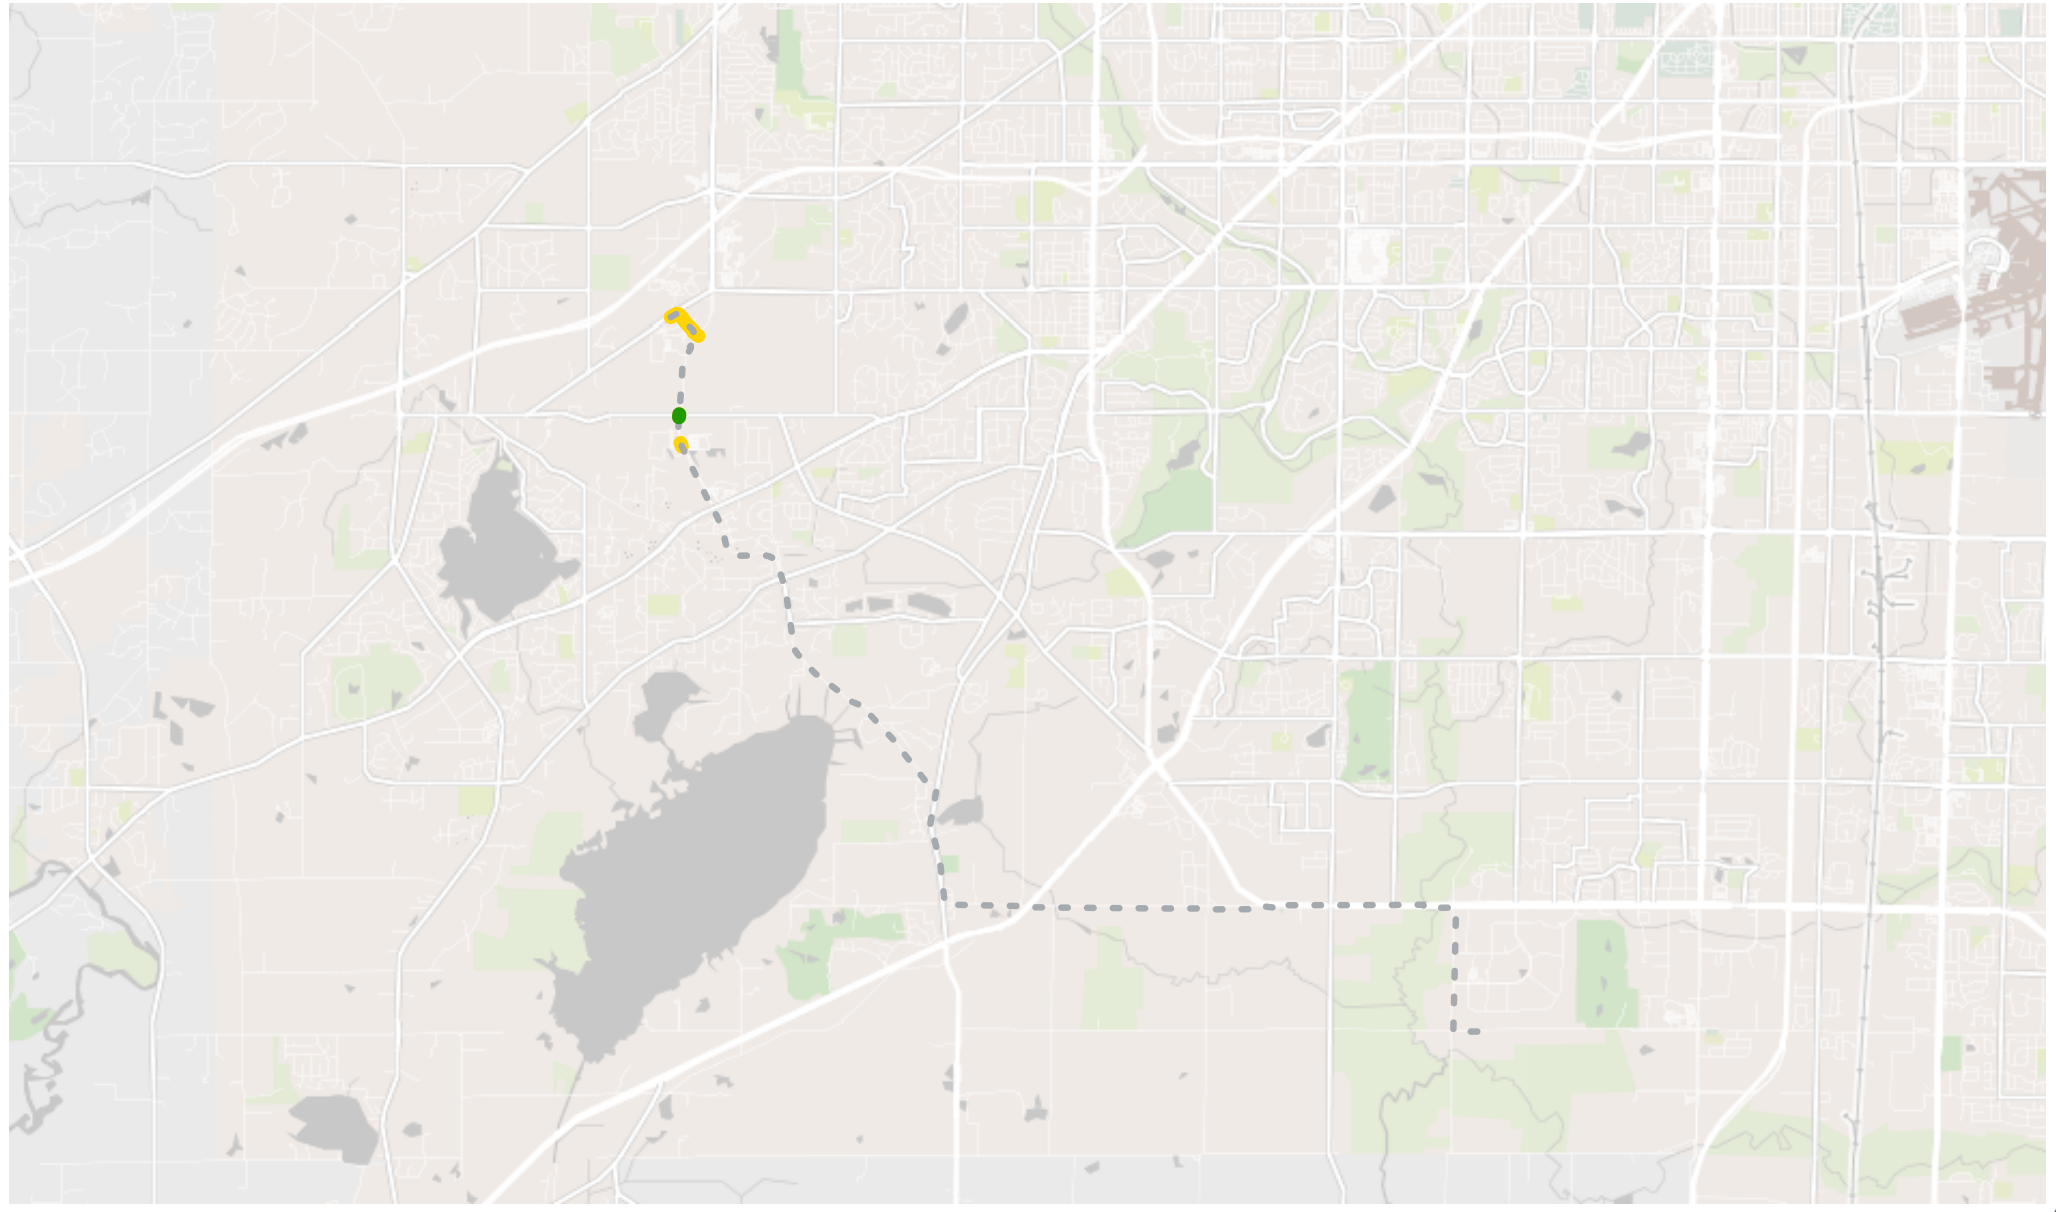

- Pipeline Route
- Installed Pipeline
- Forecast Construction
