



GREAT WATER ALLIANCE

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines

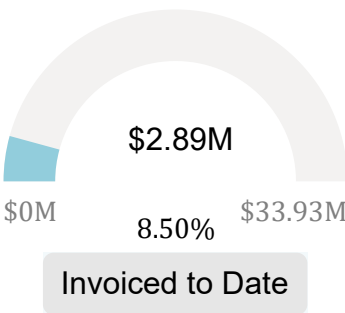


Waukesha Water Utility
Owner
Super Excavators, Inc.
General Contractor
\$33,934,739
Original Contract Amount

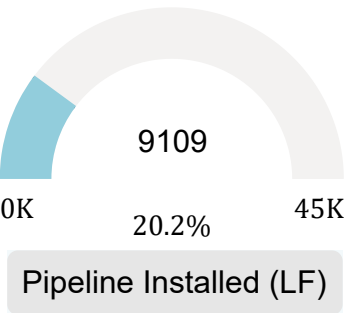


Milestone	Contract Date
Notice to Proceed	October 19, 2020
Substantial Completion	August 15, 2023
Final Completion	October 14, 2023

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	150
Days Until DOJ 50% Compliance Certification	251
Days Until DOJ Program Final Completion	601



Data current through Friday, May 14, 2021

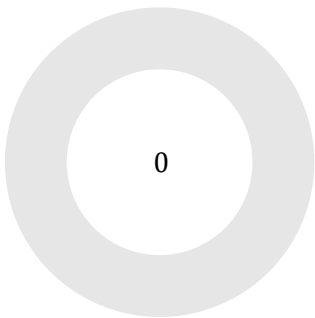


Notice of Noncompliance

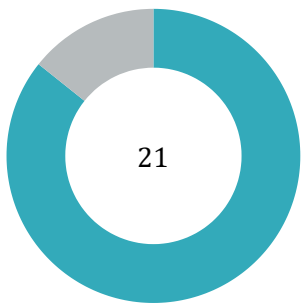

Stakeholder Engagement

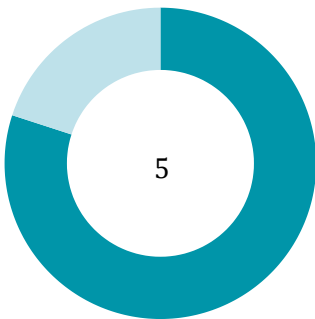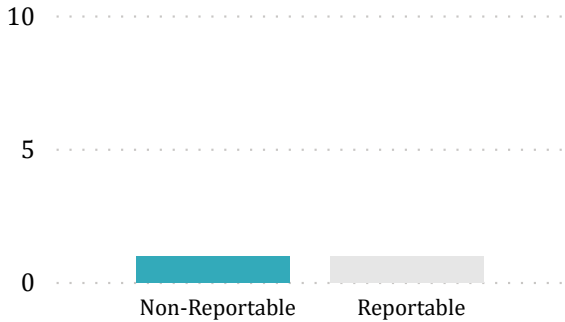


Change Orders

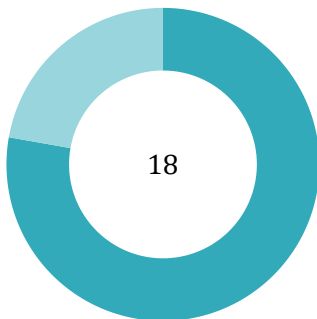

RFIs

7
Average of Turnaround

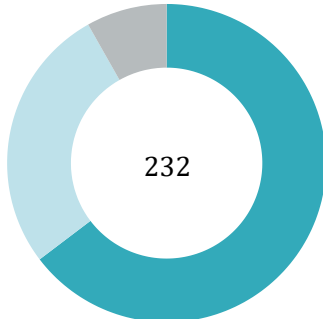

Engineering Submittals

12
Average of Turnaround
1
Excessive Reviews

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines



Data current through:

Weekly Report Ending
Friday, May 14, 2021

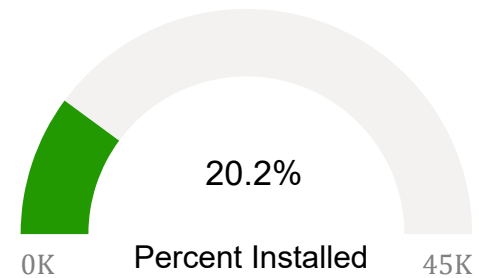


9109
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, May 14, 2021

19K
Forecast Pipe Progress (LF)

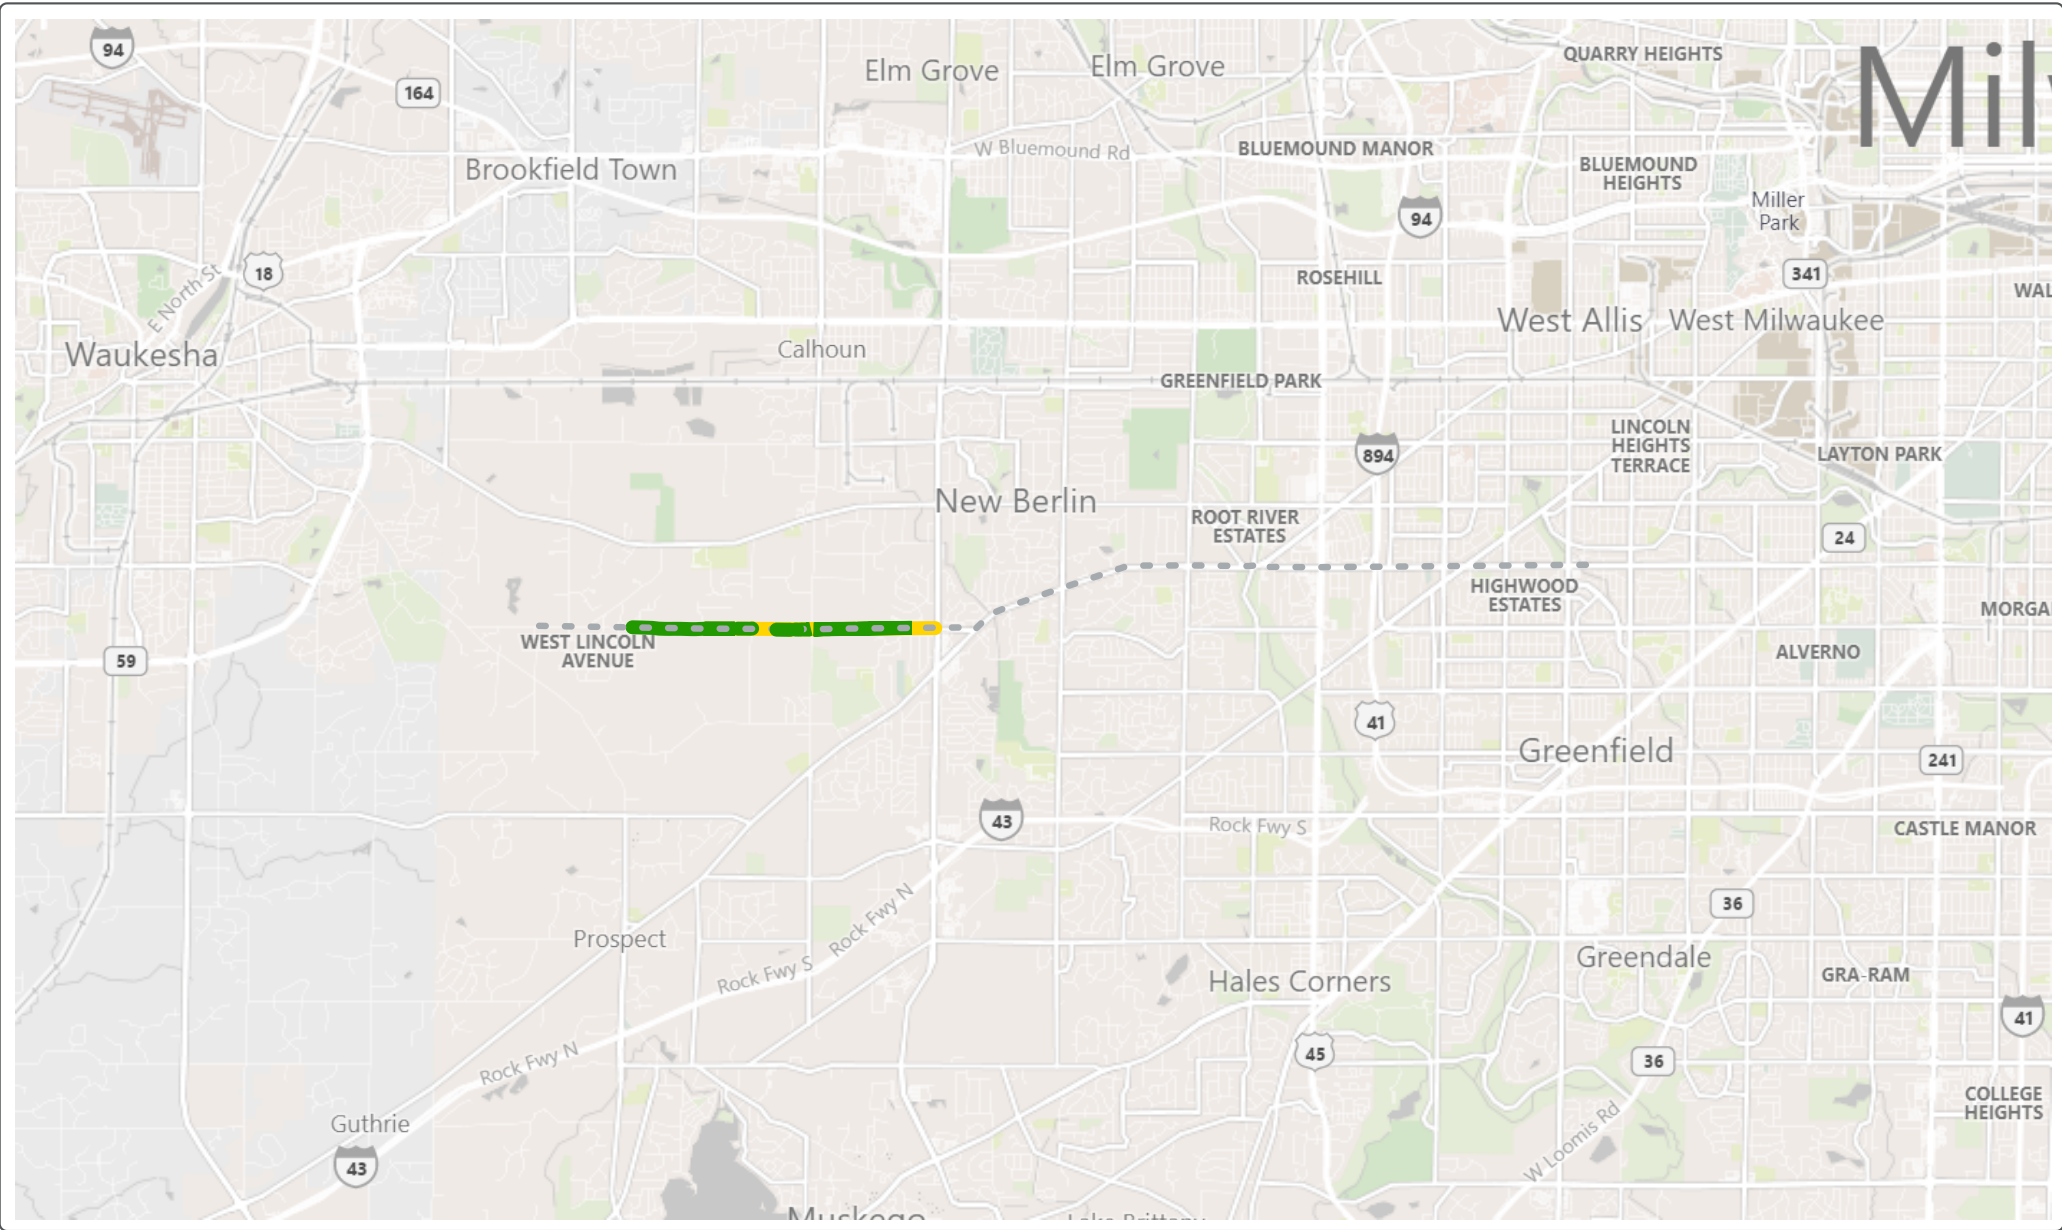

● Pipeline Route ● Installed Pipeline ● Forecast Construction

GREAT WATER ALLIANCE


CP5 - Return Flow Pipeline




Waukesha Water Utility
Owner

S. J. Louis Construction, Inc.
General Contractor

\$33,698,000
Original Contract Amount



Pipeline Installed (LF)




Invoiced to Date


Milestone	Contract Date
Notice to Proceed	July 1, 2020
Substantial Completion	March 23, 2022
Final Completion	May 22, 2022

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	228
Days Until DOJ 50% Compliance Certification	251
Days Until DOJ Program Final Completion	601


Data current through Friday, May 14, 2021

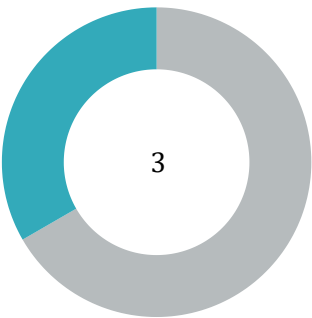


Notice of Noncompliance

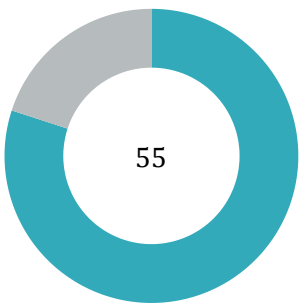


Stakeholder Engagement

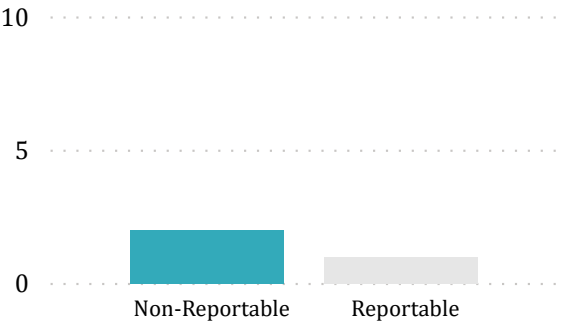

Safety

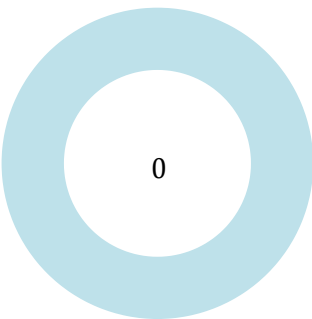


Change Orders

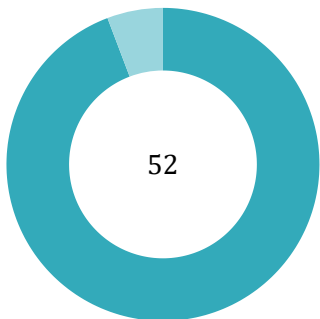

RFIs

4
Average of Turnaround

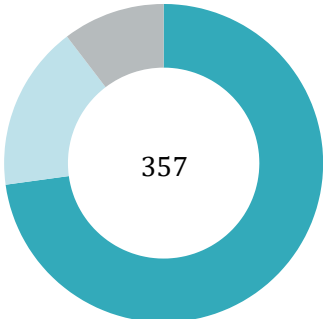

Engineering Submittals

13
Average of Turnaround
5
Excessive Reviews

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP5 - Return Flow Pipeline



Data current through:

Weekly Report Ending
Friday, May 14, 2021

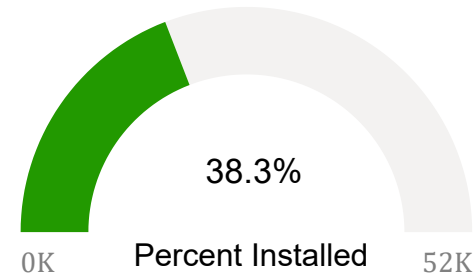


20K
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, May 14, 2021

51K
Forecast Pipe Progress (LF)

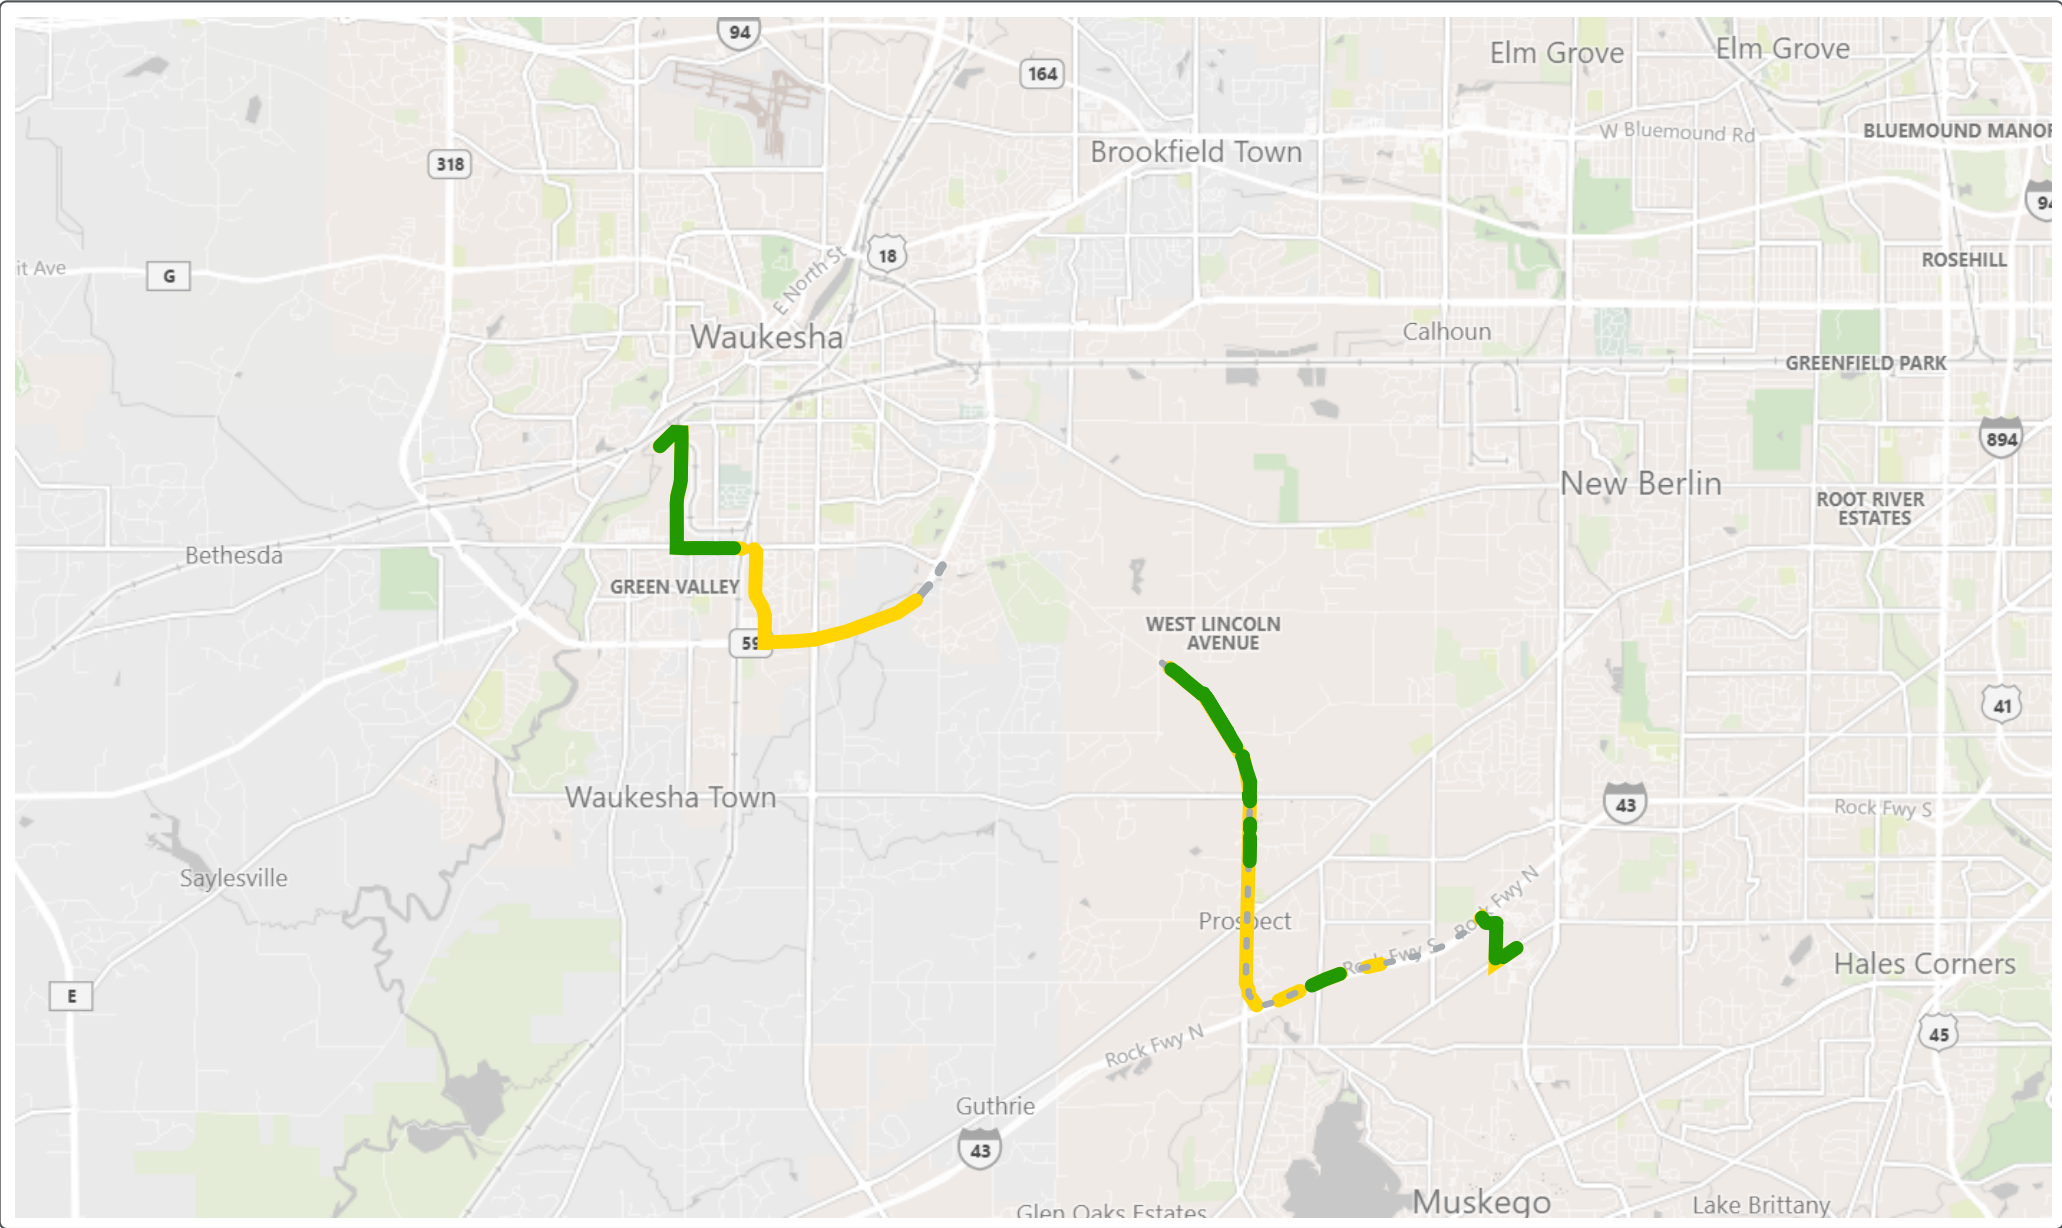

- Pipeline Route
- Installed Pipeline
- Forecast Construction

GREAT WATER ALLIANCE

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities



Waukesha Water Utility


Owner

S. J. Louis Construction, Inc.


General Contractor

\$59,209,250

Original Contract Amount



Pipeline Installed (LF)




Invoiced to Date


Milestone	Contract Date
Notice to Proceed	July 1, 2020
Substantial Completion	April 22, 2022
Final Completion	June 21, 2022

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	228
Days Until DOJ 50% Compliance Certification	251
Days Until DOJ Program Final Completion	601


Data current through Friday, May 14, 2021

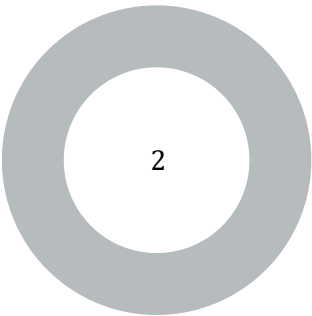


Notice of Noncompliance

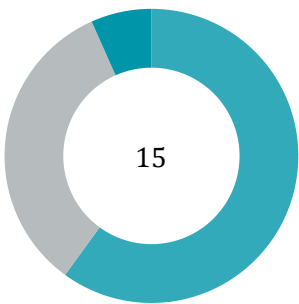


Stakeholder Engagement

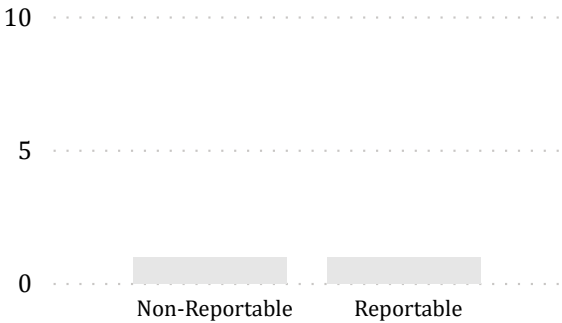

Safety

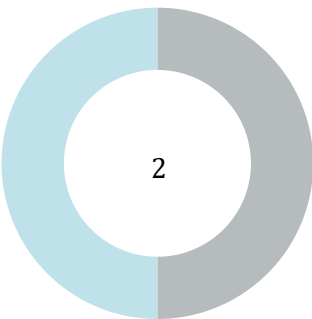


Change Orders

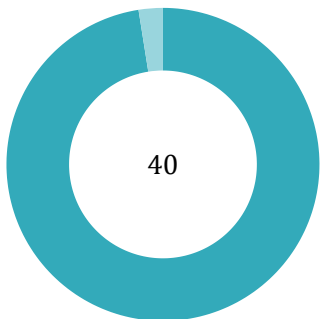

RFIs

4
Average of Turnaround

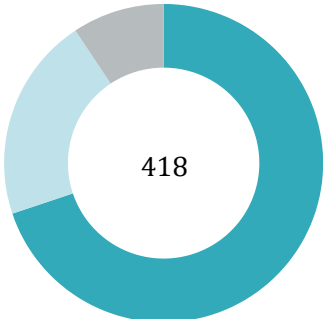

Engineering Submittals

14
Average of Turnaround
3
Excessive Reviews

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities



Data current through:

Weekly Report Ending
Friday, May 14, 2021

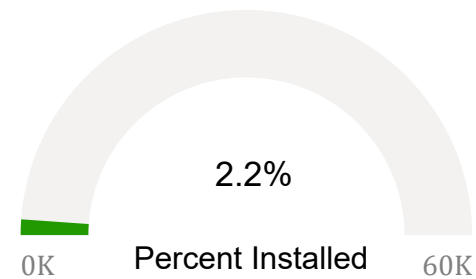


1329
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, May 14, 2021

2289
Forecast Pipe Progress (LF)

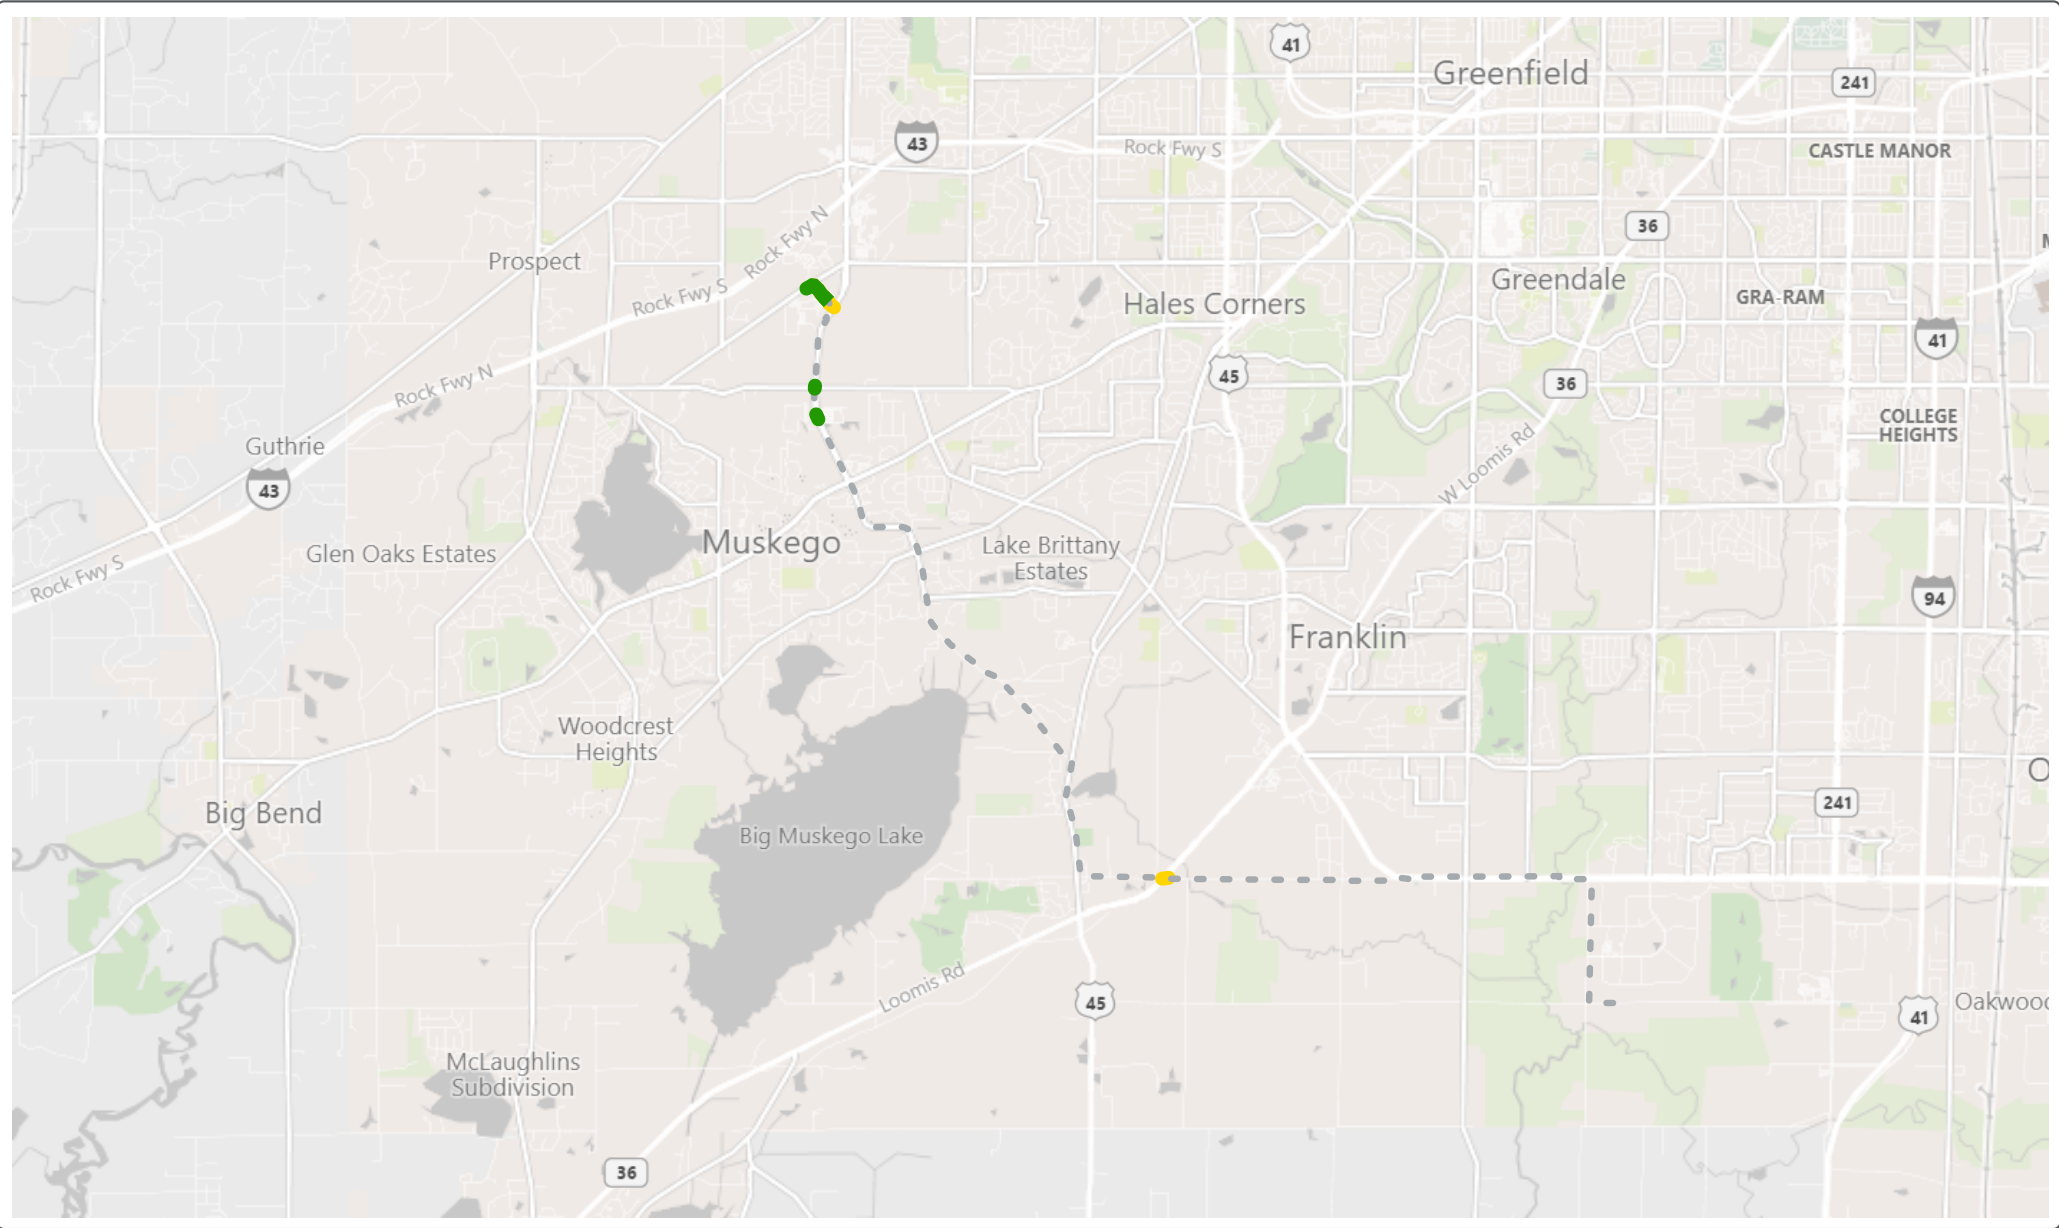

● Pipeline Route ● Installed Pipeline ● Forecast Construction
