



GREAT WATER ALLIANCE

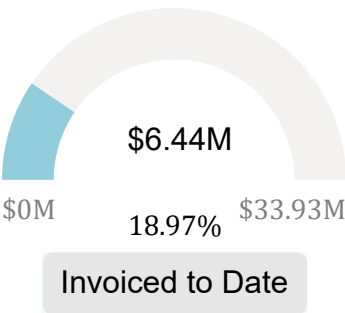

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines


Waukesha Water Utility
Owner
Super Excavators, Inc.
General Contractor
\$33,934,739
Original Contract Amount

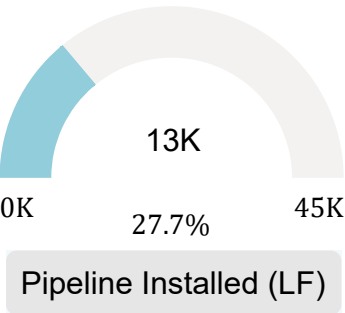


Milestone	Contract Date
Notice to Proceed	October 19, 2020
Substantial Completion	August 15, 2023
Final Completion	October 14, 2023

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	170
Days Until DOJ 50% Compliance Certification	231
Days Until DOJ Program Final Completion	581



Data current through Friday, June 11, 2021

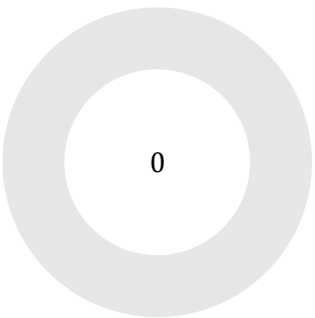


Notice of Noncompliance

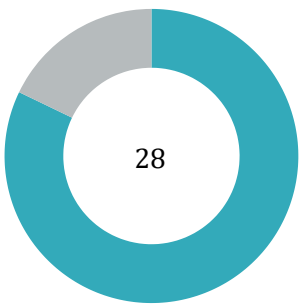

Stakeholder Engagement

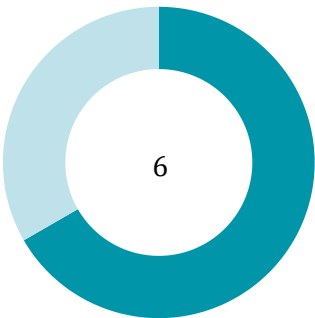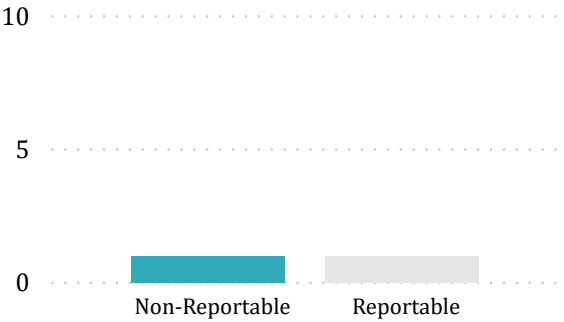


Change Orders

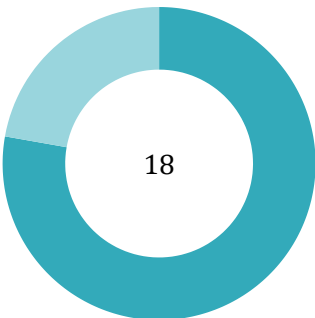

RFIs

7
Average of Turnaround

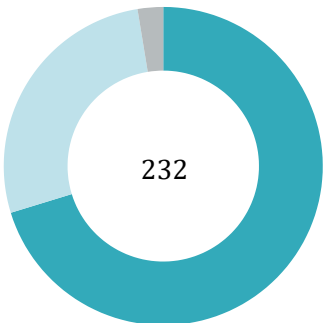

Engineering Submittals

11
Average of Turnaround
1
Excessive Reviews

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines



Data current through:

Weekly Report Ending
Friday, June 11, 2021

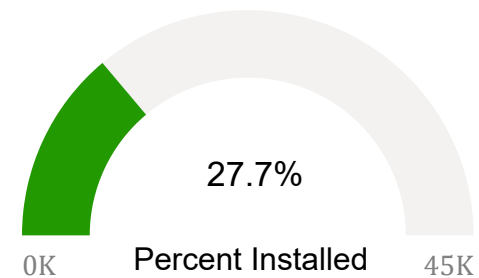


13K
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, June 11, 2021

19K
Forecast Pipe Progress (LF)

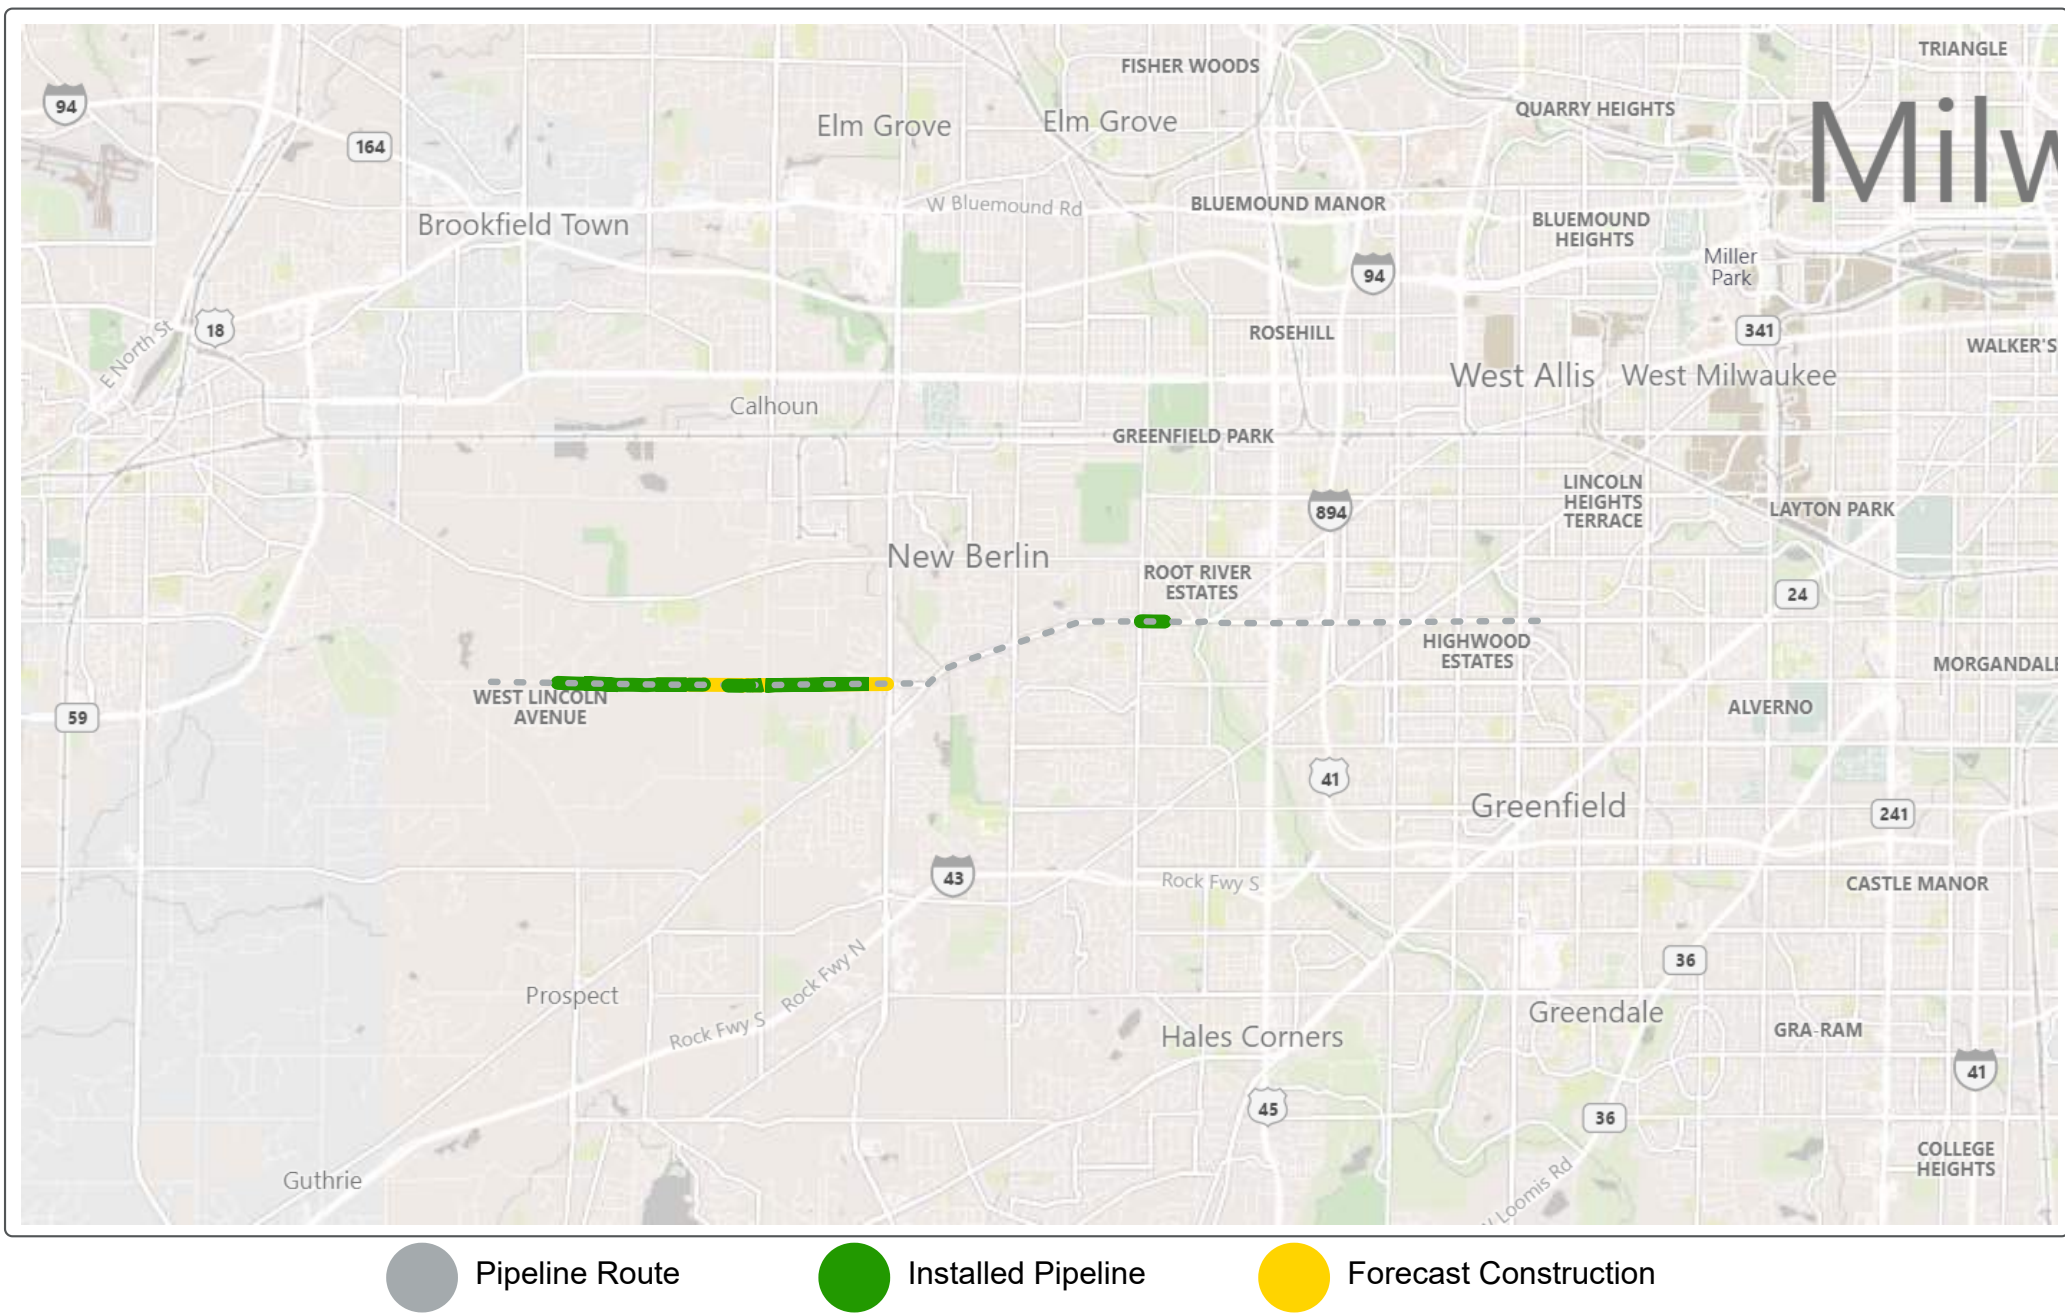

GREAT WATER ALLIANCE

CP5 - Return Flow Pipeline



Waukesha Water Utility


Owner

S. J. Louis Construction, Inc.

General Contractor


\$33,698,000

Original Contract Amount



0K 50.2% 52K

Pipeline Installed (LF)




\$0M 32.02% \$33.7M

Invoiced to Date


Milestone	Contract Date
Notice to Proceed	July 1, 2020
Substantial Completion	March 23, 2022
Final Completion	May 22, 2022

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	248
Days Until DOJ 50% Compliance Certification	231
Days Until DOJ Program Final Completion	581


Data current through Friday, June 11, 2021

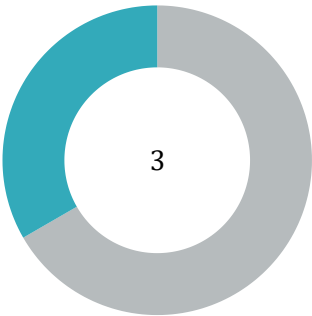


Notice of Noncompliance

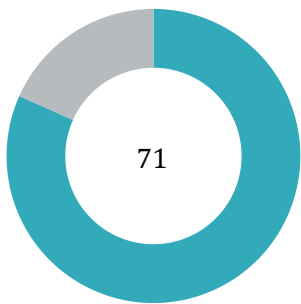


Stakeholder Engagement

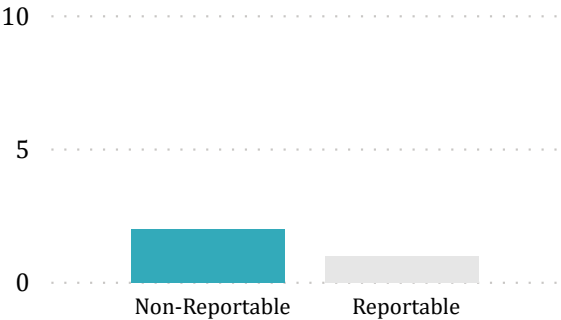

Safety

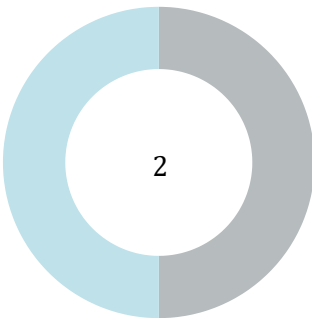


Change Orders

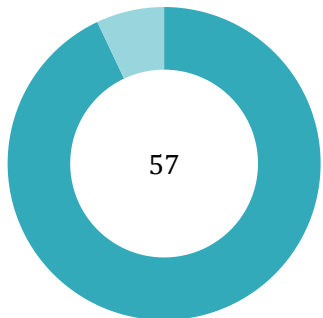

RFIs

3
Average of Turnaround

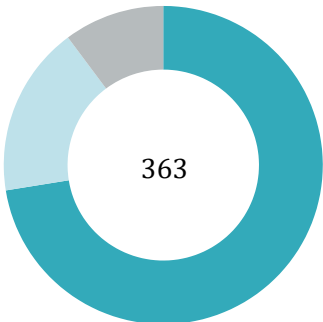

Engineering Submittals

13
Average of Turnaround
5
Excessive Reviews

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP5 - Return Flow Pipeline



Data current through:

Weekly Report Ending
Friday, June 11, 2021

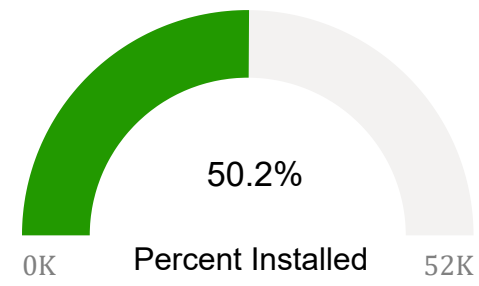


26K
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, June 11, 2021

51K
Forecast Pipe Progress (LF)

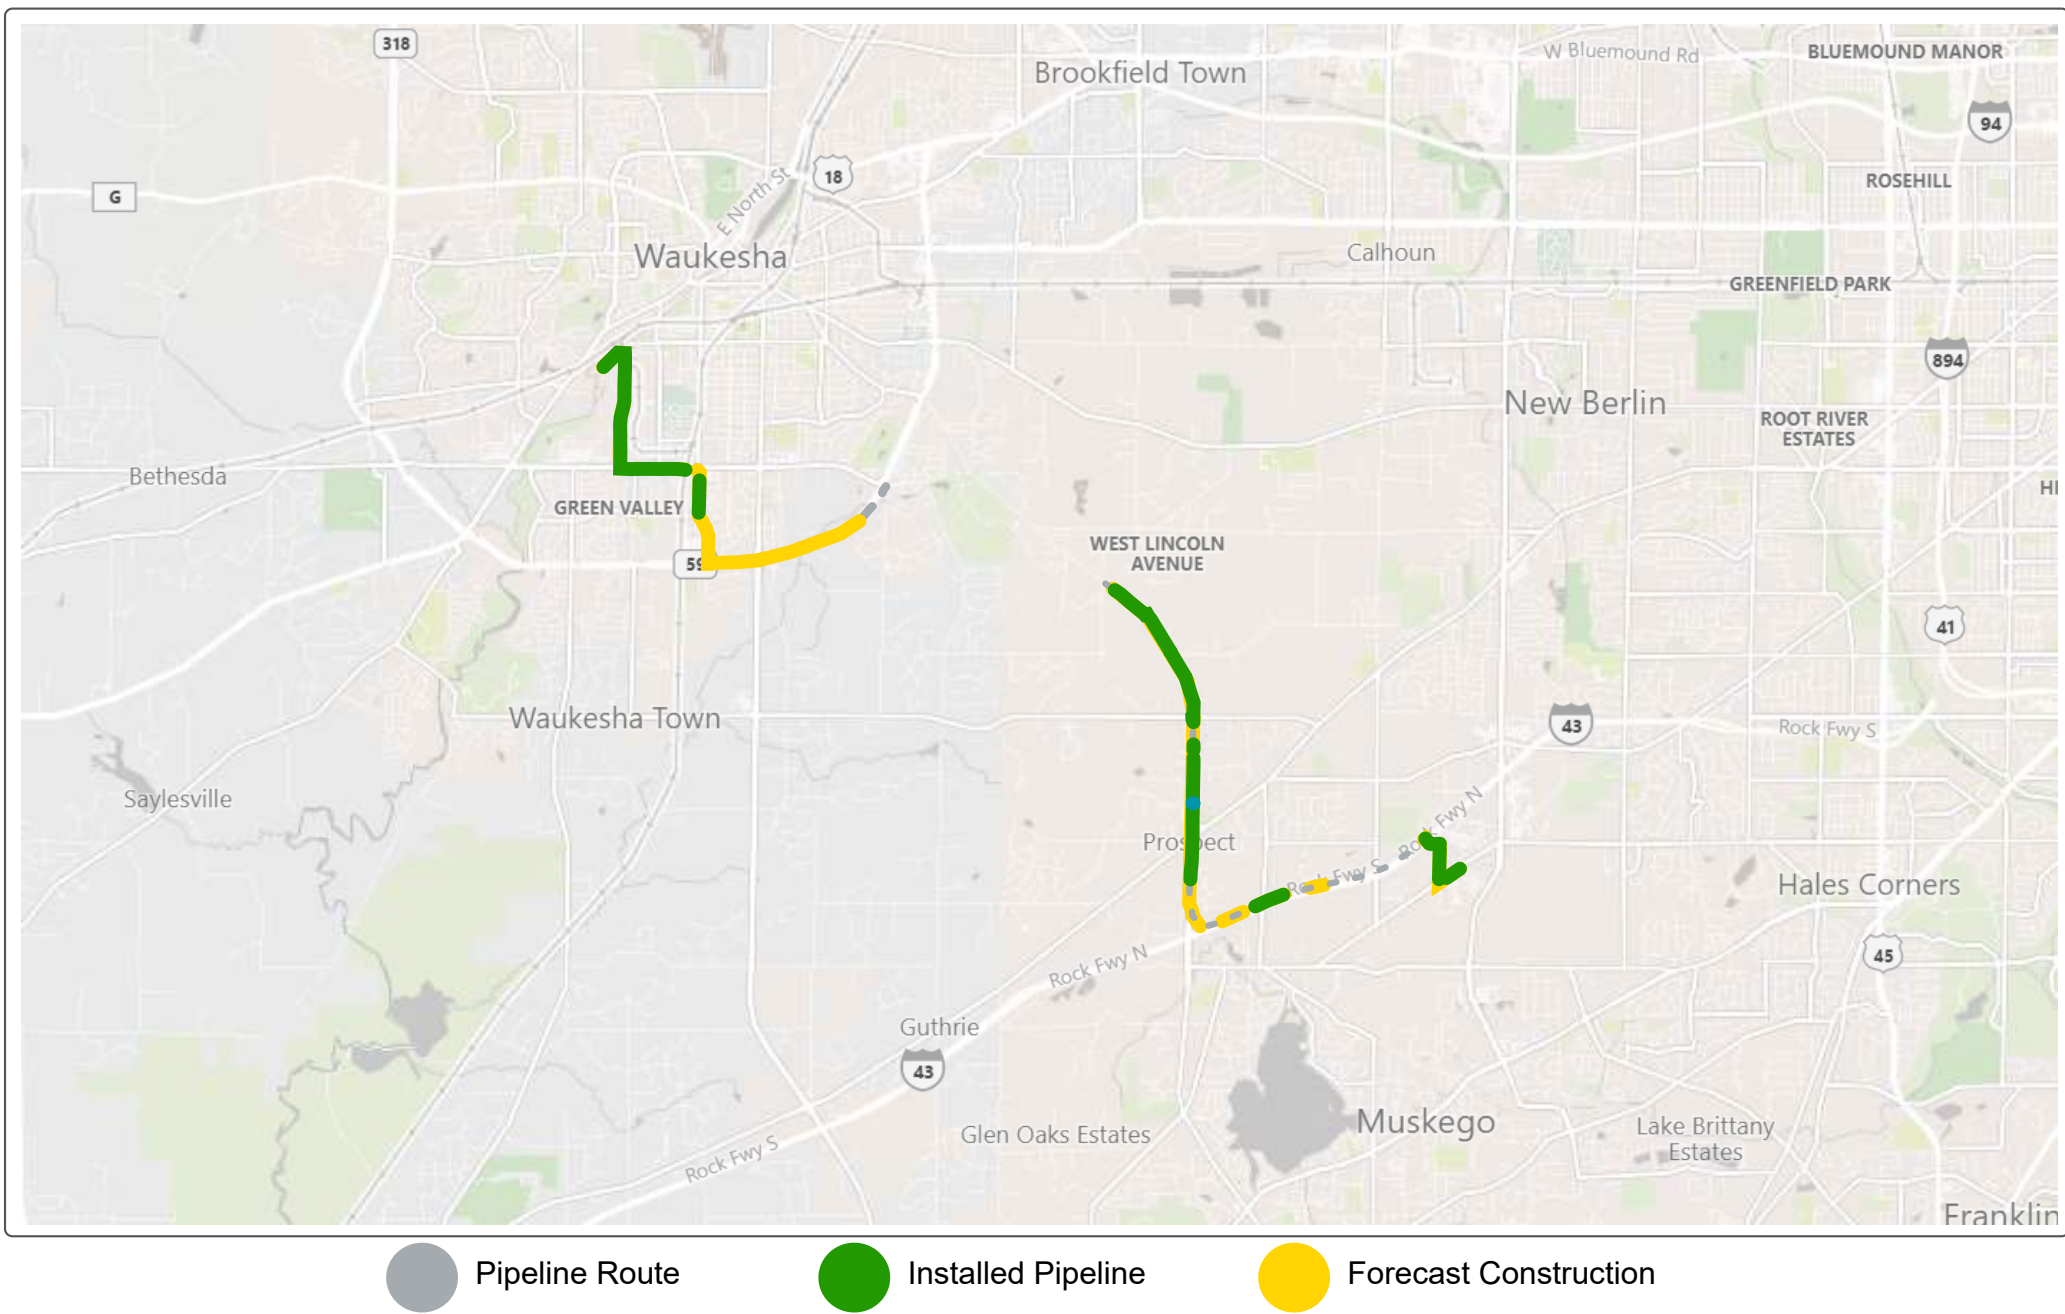

GREAT WATER ALLIANCE

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities



Waukesha Water Utility


Owner

S. J. Louis Construction, Inc.


General Contractor

\$59,209,250

Original Contract Amount



Pipeline Installed (LF)




Invoiced to Date


Milestone	Contract Date
Notice to Proceed	July 1, 2020
Substantial Completion	April 22, 2022
Final Completion	June 21, 2022

Milestone Progression	Work Days
Days Added by Change Order	0
Days Since Notice to Proceed	248
Days Until DOJ 50% Compliance Certification	231
Days Until DOJ Program Final Completion	581


Data current through Friday, June 11, 2021

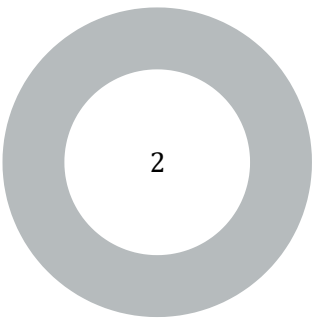


Notice of Noncompliance

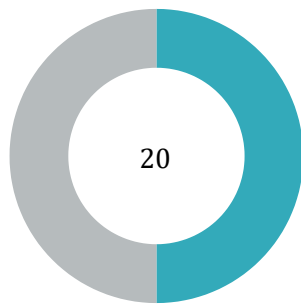


Stakeholder Engagement

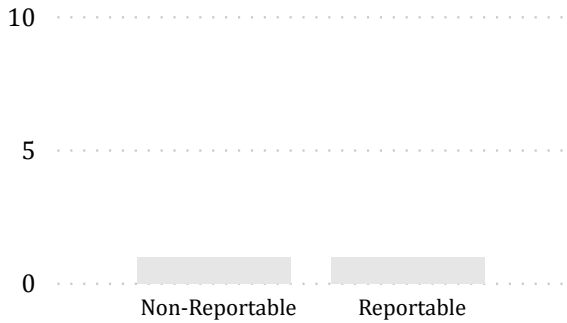

Safety

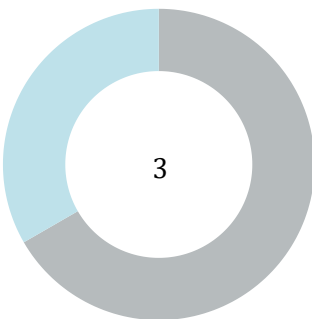


Change Orders

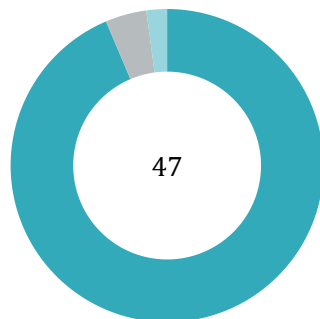

RFIs

4
Average of Turnaround

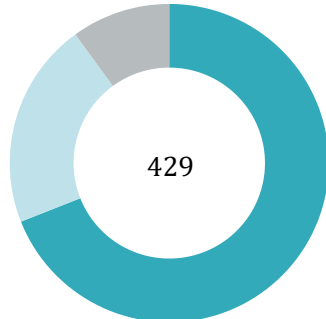

Engineering Submittals

12
Average of Turnaround
3
Excessive Reviews

None at this time Open, Submitted Pending Closed, Approved Rejected, Withdrawn


PIPELINE PROGRESS

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities



Data current through:

Weekly Report Ending
Friday, June 11, 2021

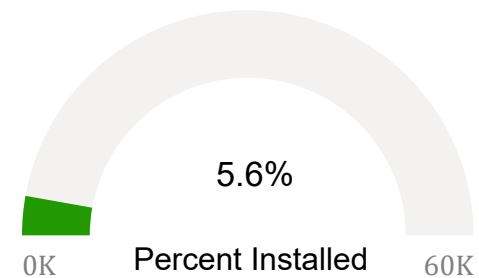

3339
Pipe Progress (LF)

Data current through:

5-Week Look Ahead
Friday, June 11, 2021

4789
Forecast Pipe Progress (LF)

