



Waukesha Water Utility  
Owner  
Super Excavators, Inc.  
General Contractor  
\$33,934,739  
Original Contract Amount



Pipeline Installed (LF)




Invoiced to Date

Milestone	Contract Date
Substantial Completion	August 15, 2023
Notice to Proceed	October 19, 2020
Final Completion	October 14, 2023


Milestone Progression	Calendar Days
Days Added by Change Order	0
Days Since Notice to Proceed	262
Days Until DOJ 50% Compliance Certification	297
Days Until DOJ Program Final Completion	785




Notice of Noncompliance

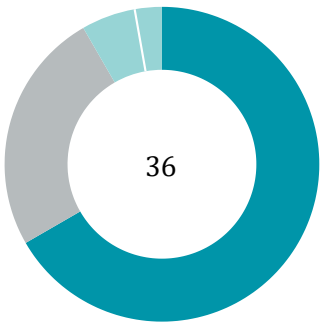


Stakeholder Engagement



Safety




Change Orders



RFIs

7.47  
Average of Turnaround

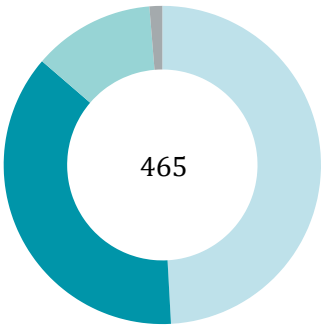

Engineering Submittals

1  
Excessive Reviews

None at this time Open, Submitted Draft Closed, Approved Rejected, Withdrawn


# PIPELINE PROGRESS

CP2A - Water Supply Pipeline Section I, II, and III, and Station Suction Pipelines



Data current through:

Weekly Report Ending  
Saturday, July 10, 2021

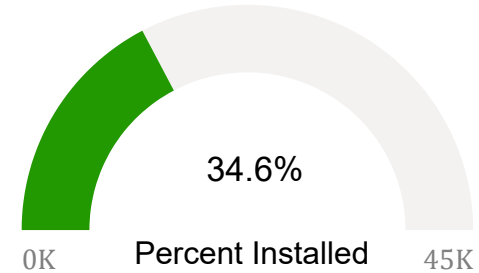


16K  
Pipe Progress (LF)

Data current through:


5-Week Look Ahead  
Saturday, July 10, 2021

19K  
Forecast Pipe Progress (LF)

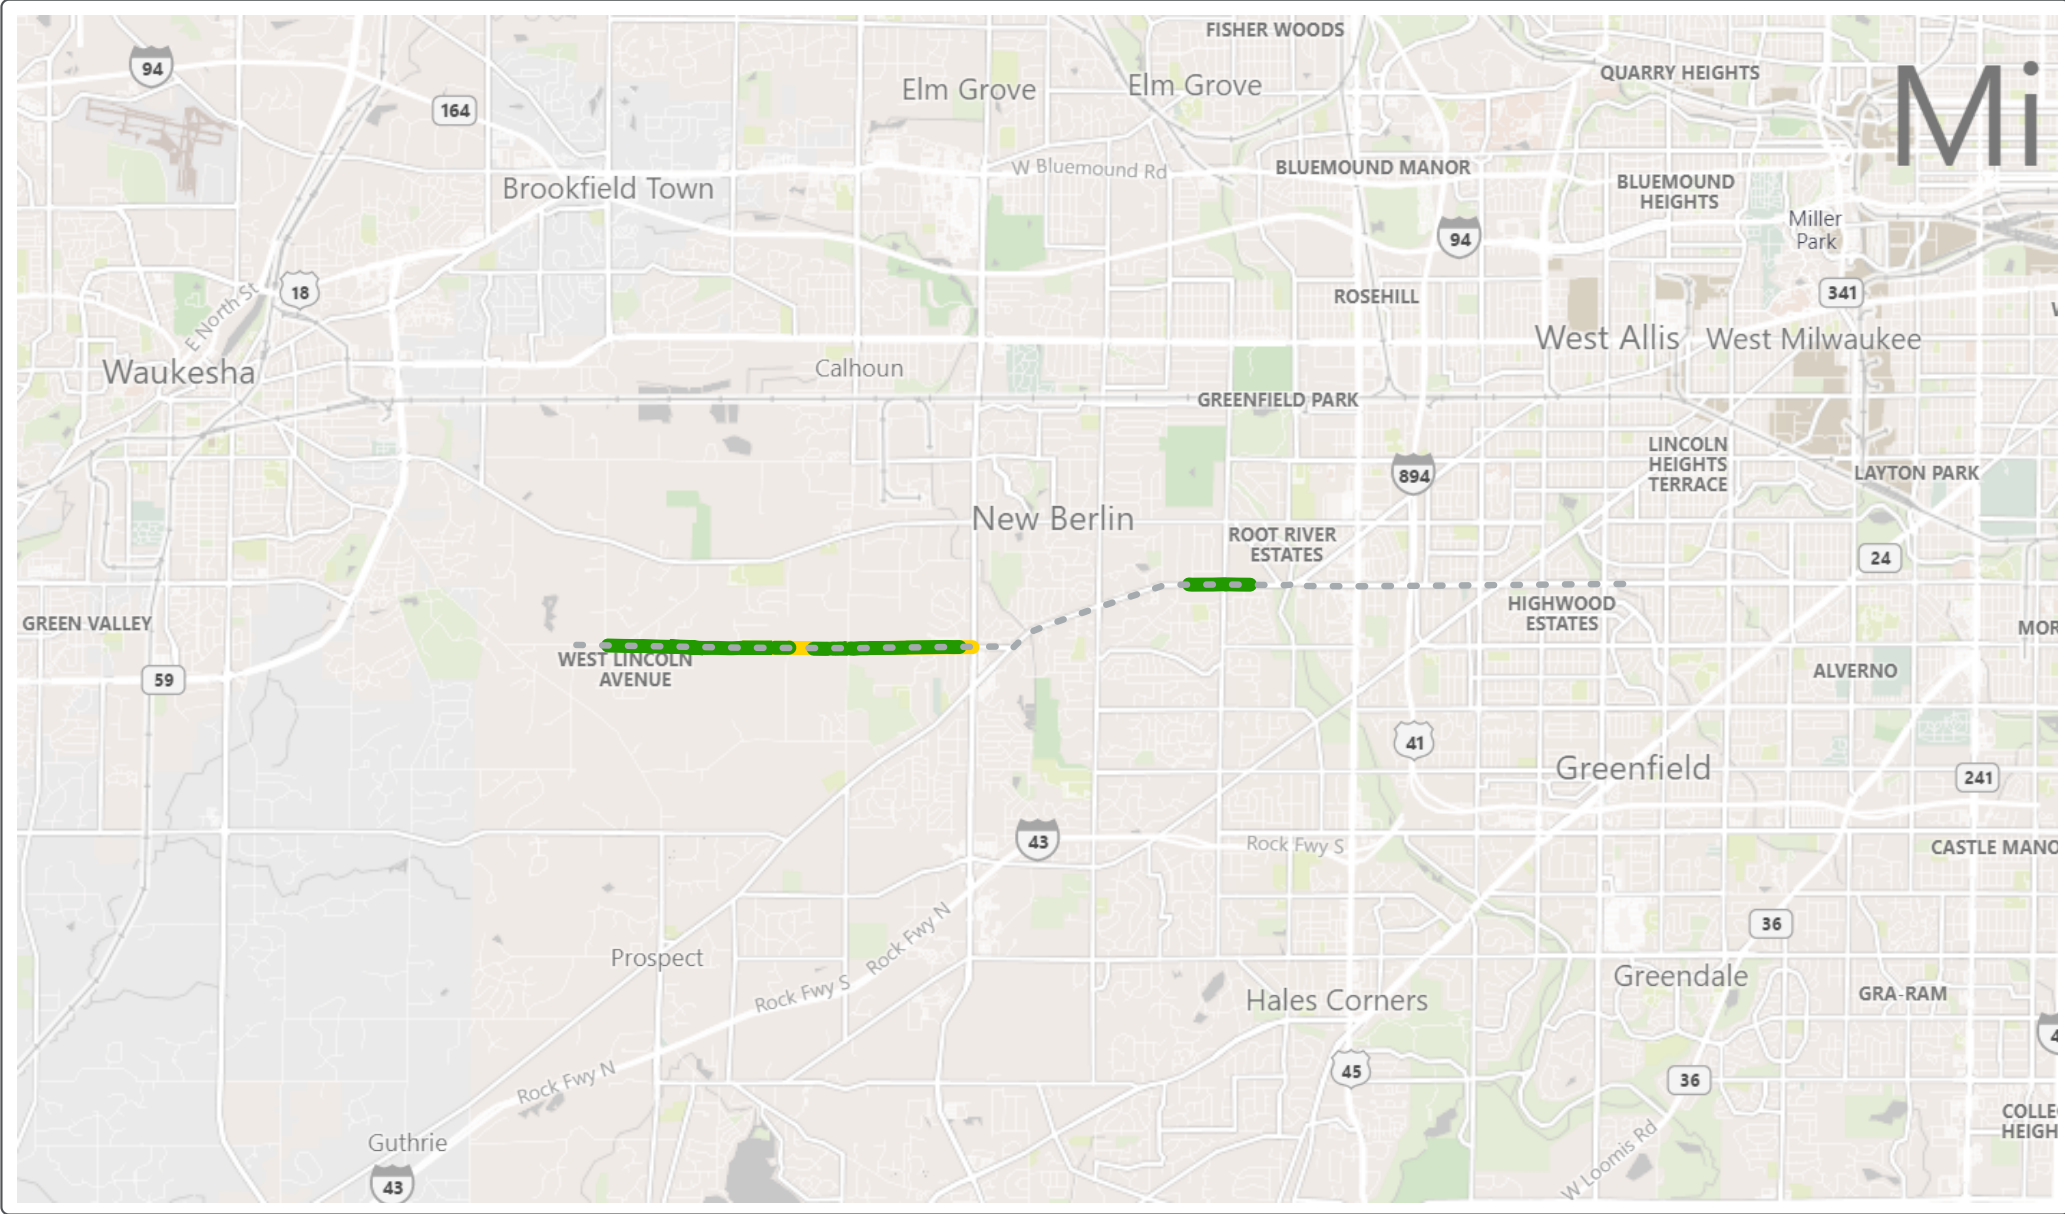


Pipeline Route    Installed Pipeline    Forecast Construction

Waukesha Water Utility  
Owner  
S.J. Louis Construction, Inc.  
General Contractor  
\$33,698,000  
Original Contract Amount




Pipeline Installed (LF)





Invoiced to Date

Milestone	Contract Date
Substantial Completion	March 23, 2022
Notice to Proceed	July 01, 2020
Final Completion	May 22, 2022


Milestone Progression	Calendar Days
Days Added by Change Order	
Days Since Notice to Proceed	372
Days Until DOJ 50% Compliance Certification	297
Days Until DOJ Program Final Completion	785

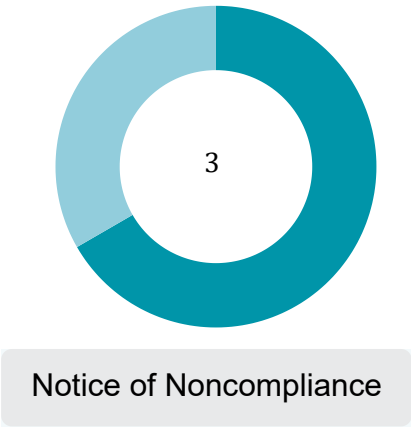

Notice of Noncompliance

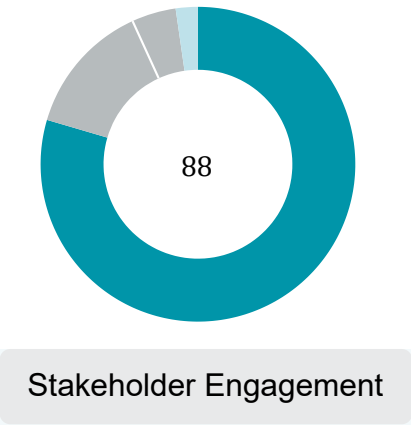

Stakeholder Engagement

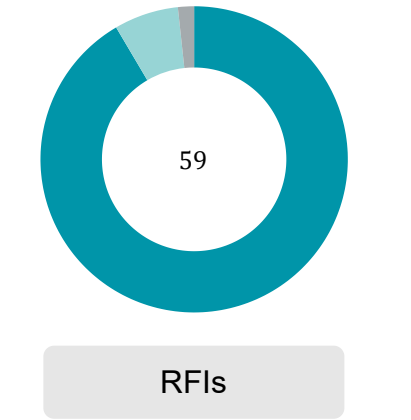


RFIs

3.37  
Average of Turnaround



Safety

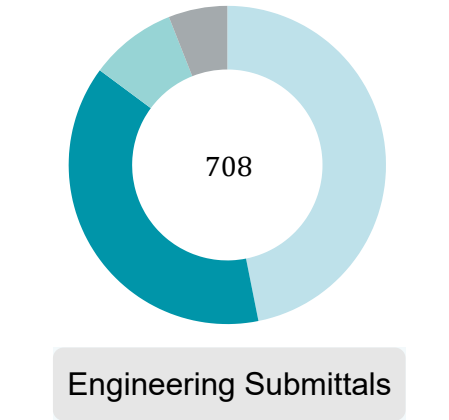

Engineering Submittals

4  
Excessive Reviews

None at this time Open, Submitted Draft Closed, Approved Rejected, Withdrawn


# PIPELINE PROGRESS

CP5 - Return Flow Pipeline



Data current through:

Weekly Report Ending  
Saturday, July 10, 2021

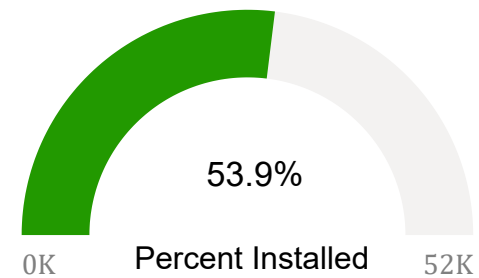


28K  
Pipe Progress (LF)

Data current through:

5-Week Look Ahead  
Saturday, July 10, 2021


51K  
Forecast Pipe Progress (LF)

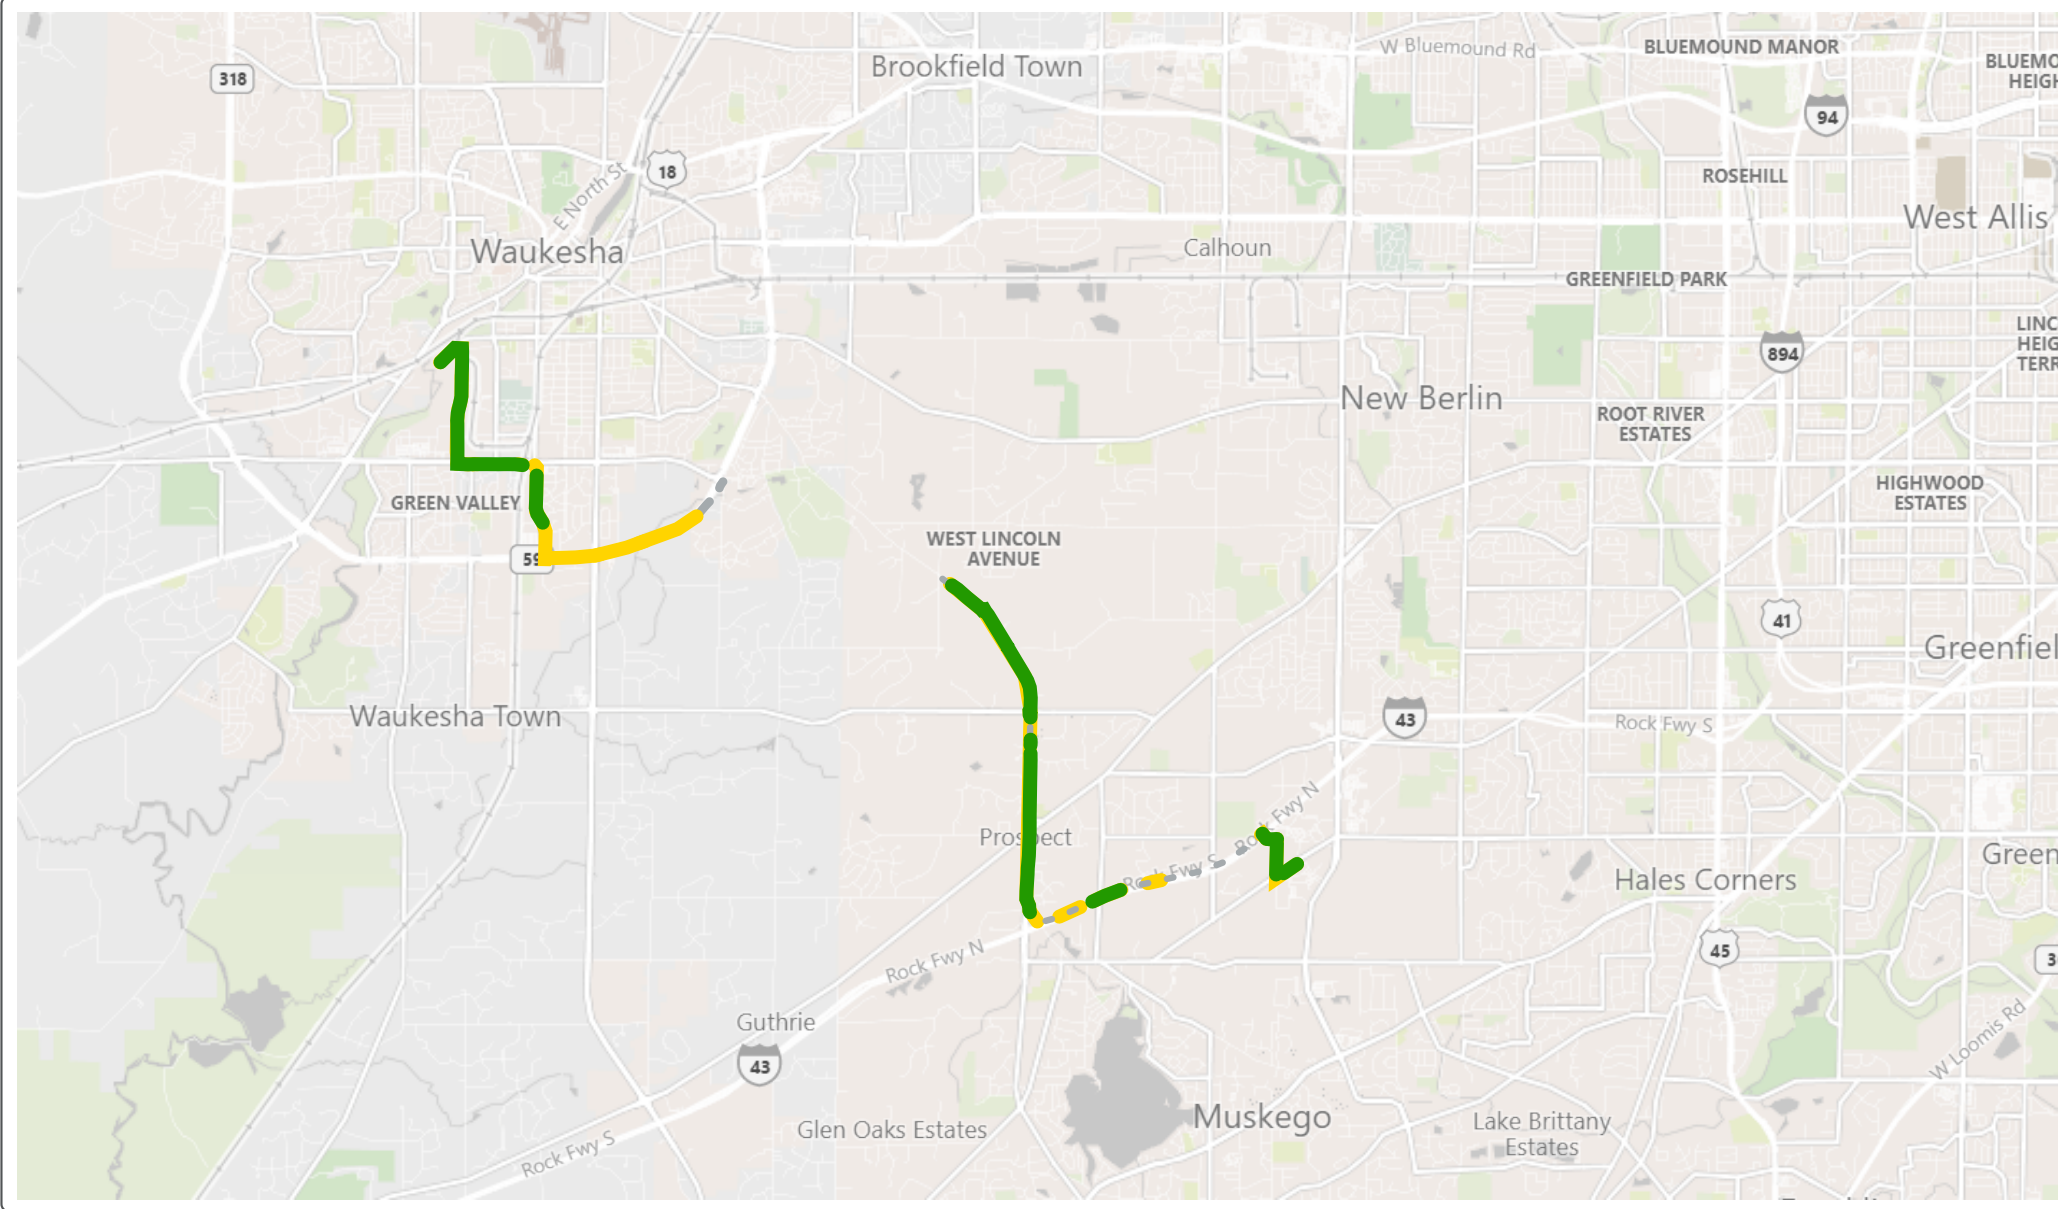

● Pipeline Route      ● Installed Pipeline      ● Forecast Construction








Waukesha Water Utility  
Owner  
S.J. Louis Construction, Inc.  
General Contractor  
\$59,209,250  
Original Contract Amount

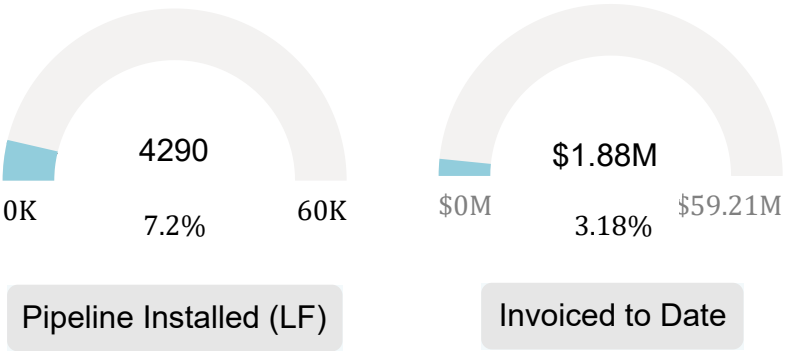


Milestone	Contract Date
Substantial Completion	April 22, 2022
Notice to Proceed	July 01, 2020
Final Completion	June 21, 2022

Milestone Progression	Calendar Days
Days Added by Change Order	0
Days Since Notice to Proceed	372
Days Until DOJ 50% Compliance Certification	297
Days Until DOJ Program Final Completion	785

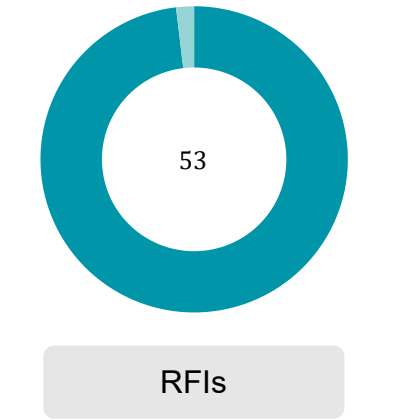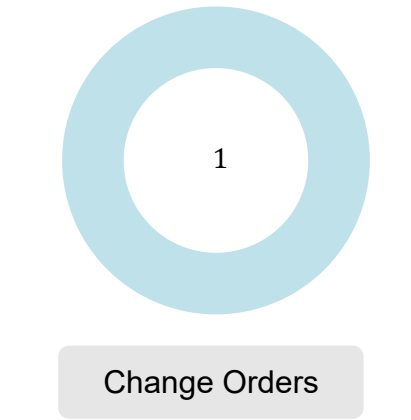

4.60  
Average of Turnaround

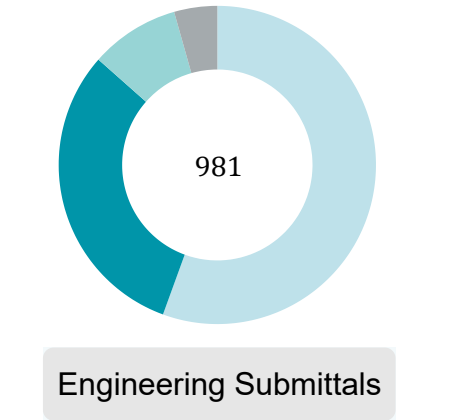

6  
Excessive Reviews

None at this time    Open, Submitted    Draft    Closed, Approved    Rejected, Withdrawn


# PIPELINE PROGRESS

CP6 - Return Flow Pipeline, 18-Inch Sanitary Sewer and Outfall Facilities



Data current through:

Weekly Report Ending  
Saturday, July 10, 2021

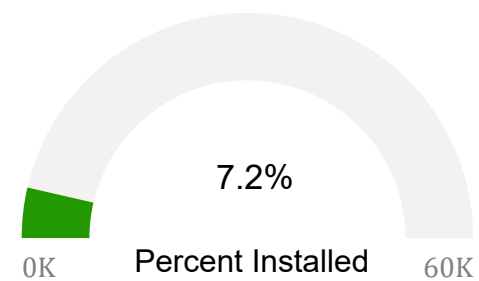


4290  
Pipe Progress (LF)

Data current through:

5-Week Look Ahead  
Saturday, July 10, 2021

5789  
Forecast Pipe Progress (LF)

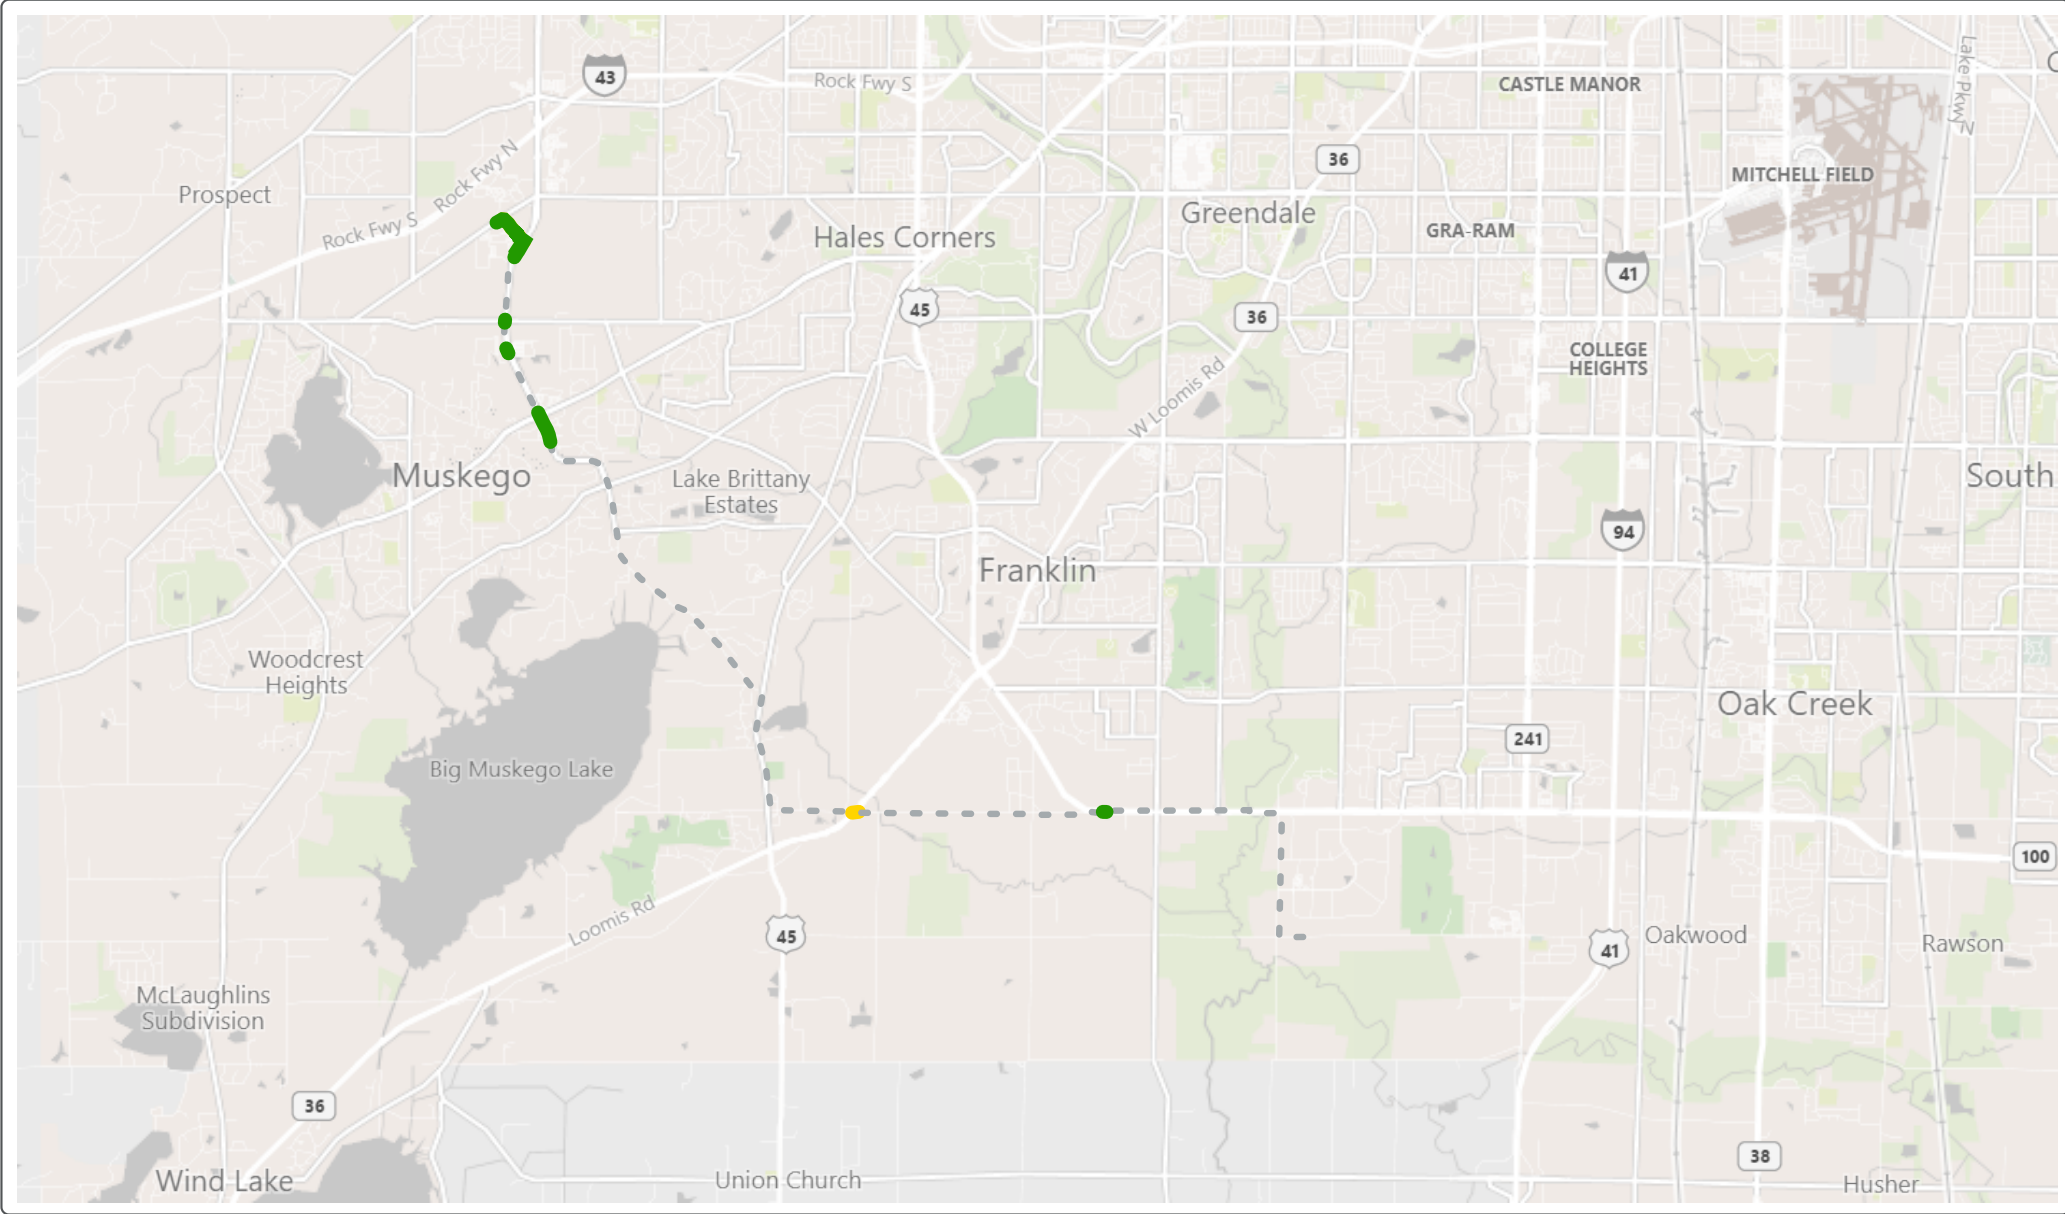

- Pipeline Route
- Installed Pipeline
- Forecast Construction
