



TUFF SHED

Quote

Location: FRANKLIN PARK | #420 | 847-768-1505

Scheduled Date:

Factory Location: FRANKLIN PARK | #420 | 847-768-1505

Created Date: 06/30/2025

Prepared by: Darren Wenger | 4142695242 | dwenger@tuffshed.com

Customer: Lynne Robinson
p. 4145071230 | c. lynnerob54@gmail.com

Special Instructions:

JDE SO
SF Quote Q-3203255

Ship to Address: 606 Rawlins Drive
Waukesha, WI 53188

Line Item Description	Sales Price	Quantity	Promo	Add'l Disc	Total Price
Premier Pro Ranch 8 x 10	\$4,342.00	1.00	(\$300.00)	\$0.00	\$4,042.00
3' x 6'7" Double Shed Door (6')	\$529.00	1.00	(\$0.00)	\$0.00	\$529.00
Shed Anchor into Dirt - Auger or MR88	\$119.00	4.00	(\$0.00)	\$0.00	\$476.00
Roof - 6/12 Roof Pitch Upgrade	\$3.50	111.00	(\$0.00)	\$0.00	\$388.50
Transom Window (16"x8")	\$69.00	3.00	(\$0.00)	\$0.00	\$207.00
Market Adjustment	\$130.26	1.00	(\$0.00)	\$0.00	\$130.26
Custom Services: hurricane clips	\$100.00	1.00	(\$0.00)	\$0.00	\$100.00
16"x8" Wall Vent - White	\$23.00	2.00	(\$0.00)	\$0.00	\$46.00
Leveling 0"-4"	\$0.00	1.00	(\$0.00)	\$0.00	\$0.00
Pewter Gray Lifetime	\$0.00	111.00	(\$0.00)	\$0.00	\$0.00
Credit for Removal of Default Door	(\$324.00)	1.00	(\$0.00)	\$0.00	(\$324.00)
Delivery Fee	\$99.00	1.00	()	\$0.00	\$99.00


Gross Total	\$5,993.76
Discount	(\$300.00)
Net Total	\$5,693.76
Estimated Tax	\$0.00
Grand Total	\$5,693.76

The price quoted is valid through the expiration date of the promotion, but in no case shall be valid longer than seven days. Once an order has been placed, pricing is guaranteed for up to 6 months. If the installation is not completed within 6 months for any reason, Tuff Shed has the right to modify the order pricing. You will be notified regarding any price adjustment prior to installation or incurring any additional charges.


LYNNE'S CITY L.I. LYNNE ROB 54
P.W. CHARTSW 84*1



Lynne Robinson
606 Rawlins Drive
Waukesha WI 53188
Q-3203255

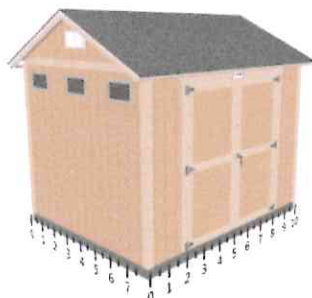


Wall D

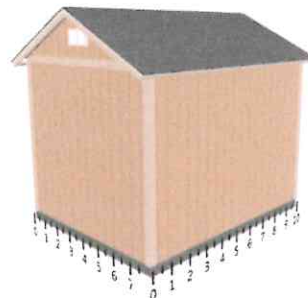

Wall C

Wall A

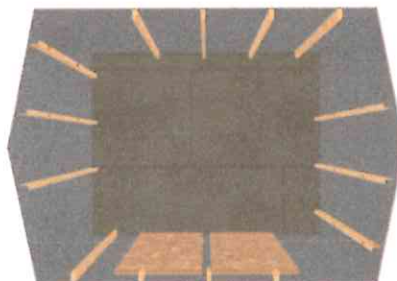

Wall B

Base Details/Permit Details

Building Size & Style

Premier Pro Ranch - 8' wide by 10' long

Paint Selection

Base: No Paint, Trim: No Paint

Roof Selection

Pewter Gray Dimensional Premium
Shingle

Drip Edge

White

Is a permit required for this job?

No, If local jurisdiction requires a permit,
fees will be added before installation
can take place

Optional Details

Doors

3' x 6'7" Double Shed Door (6')

Transoms

3 Ea Transom Window (16"x8")

Roof

111 Sq Ft Roof - 6/12 Roof Pitch
Upgrade

Floor and Foundation

4 Ea Shed Anchor into Dirt - Auger or
MR88

Vents

2 Ea 16"x8" Wall Vent - White

Custom Services

hurricane clips

Jobsite/Installer Details

Do you plan to insulate this building after
Tuff Shed installs it?

No

Is there a power outlet within 100 feet of
installation location?

Yes

The building location must be level to
properly install the building. How level
is the install location?

Within 4" of level

Will there be 18" of unobstructed
workspace around the perimeter of all
four walls?

Yes

Can the installers park their pickup truck &
trailer within approximately 200' of
your installation site?


Yes

Substrate Shed will be installed on?

Dirt/Gravel

Customer Signature: _____ Date: _____

PPR SHED UP TO 12' WIDE x UP TO 24' LONG
PREMIER PRO SERIES

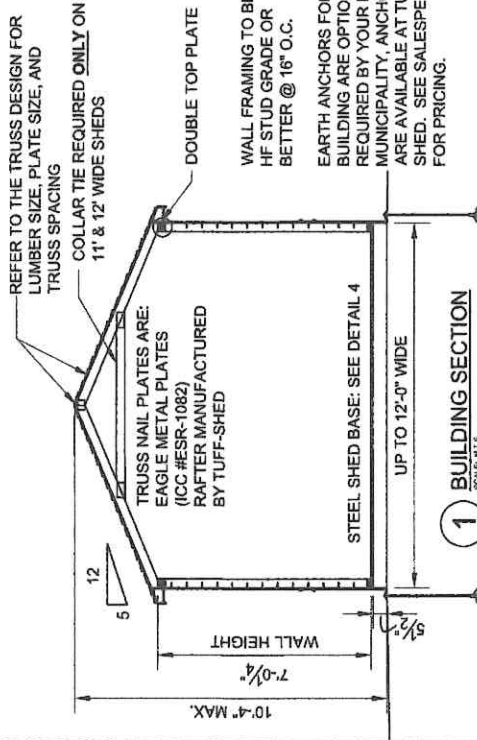

1 BUILDING SECTION
SCALE: N.T.S.

NOTES:

1. BUILDING CODE: 2022 CBC & 2022 CRC

2. DESIGN LOADING:
WIND SPEED & EXPOSURE: 110C
ROOF LIVE LOAD: 40 PSF
ROOF DEAD LOAD: 10 PSF


3. FOR SHEDS WHICH OTHERWISE MEET THE PRESCRIPTIVE REQUIREMENTS OF THE 2022 CBC & 2022 CRC ALL SHEDS CONSTRUCTED ACCORDING TO STANDARD CONVENTIONAL CONSTRUCTION METHODS.

MAILING:

ROOF:
ATTACH 7/16" SILVERCREST OSB SHEATHING TO TRUSSES WITH:
8d NAILS @ 6" O.C. AT EDGES
8d NAILS @ 12" O.C. IN FIELD


WALLS:
ATTACH 3/8" SMARTSIDE WITH FOIL BACKING TO WALL FRAMING WITH:
8d NAILS @ 6" O.C. AT EDGES,
8d NAILS @ 12" O.C. IN FIELD

HEADERS:
ATTACH HEADER TO STUD WITH:
(4) 8d TOENAIL OR (4) 16d END NAIL
DOUBLED HEADER:
16d @ 16" STAGGERED FACE NAIL

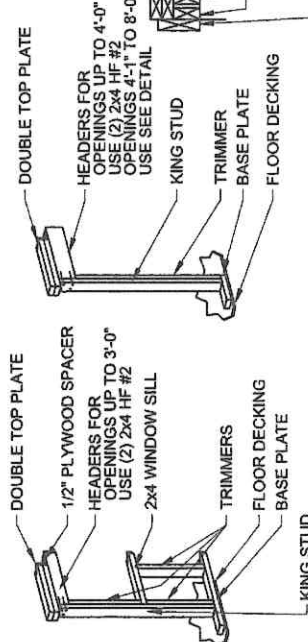


FOR WINDOW OPENINGS UP TO 3'-0" ON PREMIER PRO SERIES SIDE WALLS

2A WINDOW HEADER DETAIL FOR LOAD BEARING WALLS
SCALE: N.T.S.



FOR OPENINGS UP TO 8'-0" WIDE

3 HEADER DETAIL FOR NON-LOAD BEARING WALLS
SCALE: N.T.S.

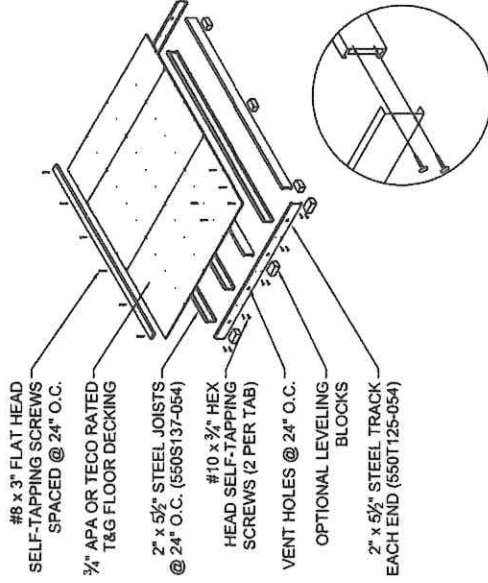

1. STEEL SHED FOUNDATION:
2" x 5/2"-16 GAUGE STEEL TRACKS G140 ZINC COATED @ 24" O.C.
2" x 5/2"-16 GAUGE STEEL JOISTS G140 ZINC COATED @ 24" O.C. (SUPPLIER: ALLIED STUDCO - JOIST: 550S137-054 / TRACK: 550T125-054).
2. 3/4" APA OR TECO RATED TONGUE AND GROOVE FLOOR DECKING. 24" MAX PANEL SPAN. STAGGER PANEL LAYOUT.
3. FASTEN FLOOR DECKING TO JOIST & TRACKS USING #8 x 1 1/2" LONG MIN. SELF-DRILLING SCREWS @ 12" O.C. NO BLOCKING REQUIRED. ALL EDGES SHALL LIE ON FLOOR JOISTS. STAGGER PANEL LAYOUT PER APA CONDITION 1.
4. FASTEN SOLE PLATE THROUGH FLOOR DECKING INTO JOISTS OR TRACKS WITH #8 x 3" GALVANIZED SELF-TAPPING SCREWS @ 24" O.C.
5. ALLOWABLE FLOOR LIVE LOAD: 75 PSF FOR STEEL JOISTS CONTINUOUSLY SUPPORTED. 50 PSF FOR JOISTS ON BLOCKS AS SHOWN.
6. USE OPTIONAL CONCRETE BLOCKS AS REQUIRED TO LEVEL BUILDING: SUGGESTED SIZES: 2' x 8' x 16", 4' x 8' x 16", OR 8' x 8' x 16". BLOCKS UNDER JOISTS SPACED @ 8'-0" O.C. MAXIMUM. BLOCKS UNDER TRACK SPACED @ 4'-0" O.C. MAXIMUM.

4 SHED BASE DETAIL
SCALE: N.T.S.

THESE DRAWINGS AND THE DESIGN ARE THE PROPERTY OF TUFF SHED, INC. THESE DRAWINGS ARE FOR A BUILDING TO BE SUPPLIED AND BUILT BY TUFF SHED. ANY OTHER USE IS FORBIDDEN BY TUFF SHED INC. & THE ENGINEER OF RECORD.

P.O. #
Drawn By: SJ
Date: 11/14/24
Checked By:
Date:
Scale: N.T.S.

Order #:
Customer:
Site Address:
Building Size: width - length - height - sq. ft. area

TUFF SHED
Storage Buildings & Garages
TUFF SHED, INC.

DRAWINGS BY:
TUFF SHED, INC.
IN HOUSE DRAFTING DEPARTMENT
1777 S. HARRISON STREET
DENVER, COLORADO 80210
(303) 753-TUFF
TUFF SHED INC. ASSUMES ALL RESPONSIBILITY FOR THE CONTENT OF THESE DRAWINGS AND THE CONSTRUCTION OF THE BUILDINGS SHOWN HEREIN.

TITLE
BUILDING SECTIONS
SHED BASE DETAILS
HEADER FRAMING DETAILS
NOTES - 2022 CBC & IRC - 1100

DRAWING NO.
PPR-01
REV. LEVEL 01
SHEET 1
PAGE 1 OF 1
